

VAN NESS

IMPROVEMENT PROJECT



Van Ness BAC
July 18



Agenda

1. Call to order. Van Ness Business Advisory Committee members please sit at table.
2. Public comment for matters within BAC jurisdiction not on today's calendar.
3. Approval of Minutes – June 20.
4. SFMTA staff updates.
5. Next meeting.

BAC administration reminder

- BAC members are asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

Public Comment


- See Public Comment Policy on back of agenda.
- Public comment for matters that are within the Van Ness Business Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes

- June 20.



Staff updates

- Project update


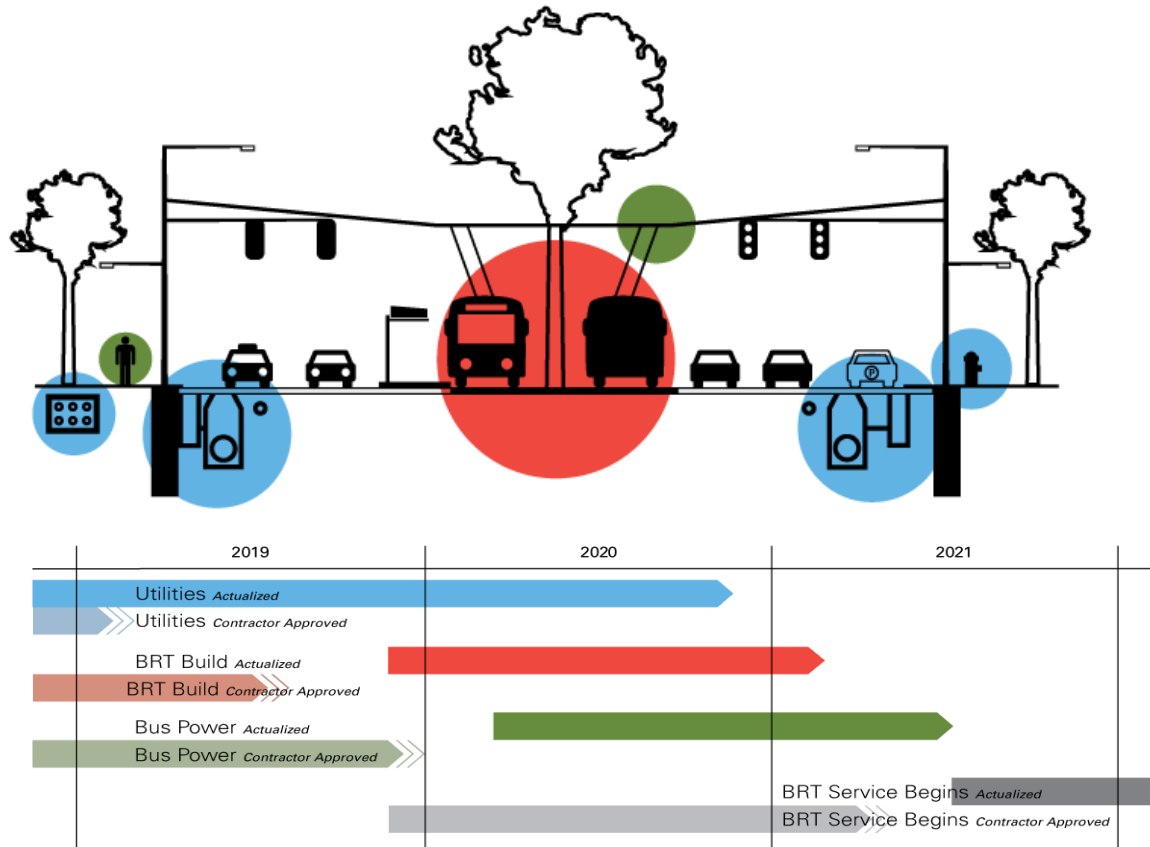


Staff Updates

- Phases 1A and 1B underway. Expected completion winter 2019



- Phases 1C and 1D scheduled summer 2019 - summer 2020





	Start	Finish
1A	Fall 2016	Summer 2019*
1B	Summer 2018	Winter 2019*
1C	Summer 2019*	Spring 2020*
1D	Winter 2019*	Summer 2020*
2	Winter 2019*	Spring 2021*
3	Summer 2020*	Summer 2021*

*Estimated

Staff Updates

- Phase 2 scheduled winter 2020 - spring 2021



- Phase 3 scheduled summer 2020 - summer 2021



	Start	Finish
1A	Fall 2016	Summer 2019*
1B	Summer 2018	Winter 2019*
1C	Summer 2019*	Spring 2020*
1D	Winter 2019*	Summer 2020*
2	Winter 2019*	Spring 2021*
3	Summer 2020*	Summer 2021*

*Estimated

Staff Updates

Traffic and utility zones shifting

- Started night of Wednesday, June 19
- Continues utility work on opposite side of Van Ness
- Utility work is halfway complete
- Traffic lane and construction zone adjustments taking place
- Meters are being be removed
- Loading and blue zones for parking with a valid disabled permit are being relocated. Map of specific locations of relocated colored curb zones can be found at SFMTA.com/VanNess
- Construction fencing being installed around new work zones

Staff Updates

Project contract modification approved by MTA Board

- Tuesday, July 16, 1:00 p.m. City Hall, Room 400
- Resolved two contractor claims for unavoidable delays resulting from water and sewer issues
- Covered by project's allocated allowances, did not increase project budget
 - SFPUC provided analysis and agreed to resolution
 - Increased the contract amount by \$4,819,650
 - Increased contract duration by 279 total calendar days
 - Of claimed 279 days unavoidable delays, 135 days are justifiable due to sewer and water issues
 - Contractor agrees to drop remaining 144 delay days claims and to avoid any litigation cost for both parties

Staff Updates

- Based on expenditures to date, construction is approximately at 34.45% completion (34% in May)
- Based on linear feet, percentage completion:

Phase	Joint Trench %	Sewer %	Water %	Roadway %	Sidewalk %
1A*	100%	100%	100%	93%	53%
1B*	85%	97%	96%	0.09%	0.04%
Total* %	40.67%	53.7%	50.69 %	30.16%	29%

*Total % complete is the most accurate estimate of the overall progress of the project.

Staff Updates

Construction update

- Traffic lane and construction zone shifts underway
- Joint trenching ongoing
- Addressing utility conflicts
- Sidewalk replacement, street base repair and paving work – outreach to affected blocks ongoing
- SFPD additional nighttime patrols and increased enforcement of construction zones



Staff Updates

Geary Rapid Project

The first phase of construction as part of the [Geary Rapid Project](#) continues. Work to replace aging water and sewer lines between Masonic Street and Van Ness Avenue is scheduled to be done in coordination with the San Francisco Public Utilities Commission (SFPUC).

For more information visit SFMTA.com/Geary or contact GearyRapid@SFMTA.com

Staff Updates

Lombard Street Vision Zero Project

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

General working hours Monday through Friday 7:00 a.m. to 3:00 p.m.

Project Completion scheduled for: June 2020

For more information visit SFPublicWorks.org/Lombard or call 415-558-5282

Business Support

- Fall Car Card Campaign in design
- “Get Inspired” will be the theme

Staff Updates

- **Recent Activities**

- Van Ness BRT Community Advisory Committee, June 25
- TA Citizen's Advisory Committee, June 26
- Traffic and Construction Zone shift outreach
 - Pop-Up Block meeting at Comfort Inn by the Bay, July 8

Staff Updates

- Outreach Updates
 - Upcoming outreach activities
 - Van Ness BRT Community Advisory Committee Meeting
 - July 25, 5:00 p.m.
 - 1 South Van Ness, Union Square Conference Room, 7th Floor
 - SFCTA Citizens Advisory Committee, July 24
 - Pop up meetings for blocks affected by construction shift by request
 - Meet the Expert: August 7, 6:00 p.m.

Next Meeting



September 19, 3:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess

