


# Quarterly Revenue Bond Oversight Committee Meeting

"Streets" Project Status Updates \*

\* All financial values based on June 2018 data.

### **Active and Recently Completed Projects**

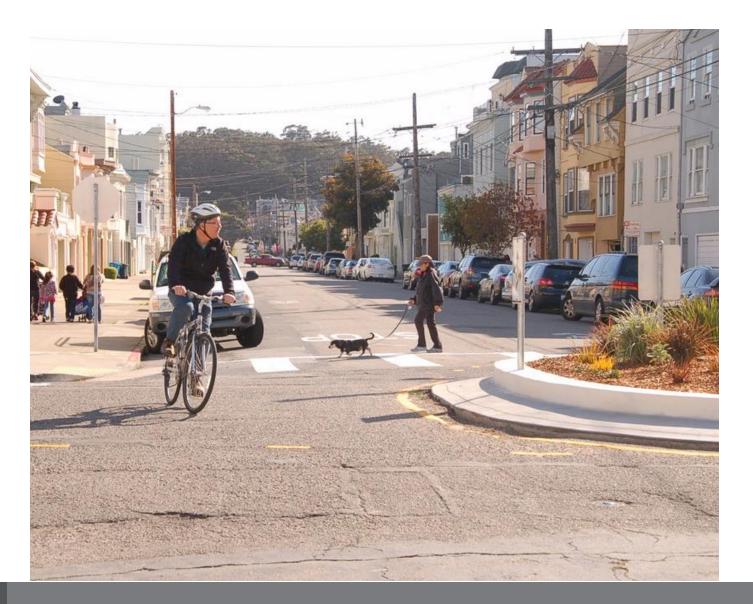




# 7th and 8th Street Streetscape Project

### **BOND STATUS**

	Allocated	Spent	Remaini ng
Series 2014	\$300,000	\$263,798	\$36,202

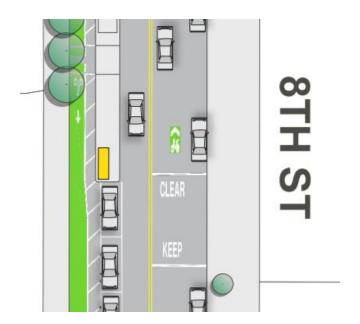

### **UPCOMING MILESTONES**

**Project Status** 

Close Out

- Waiting to close out.
- Open for use.



### **Bicycle Strategy Capital Projects** Wiggle Neighborhood Green Corridor

### **BOND STATUS**

	Allocated	Spent	Remaining
Series 2013	\$228,400	\$267,971	\$(39,572)





**Project Status** 

Close Out

- Project is complete.
- Open for use.



# **Broadway Chinatown Streetscape**

### **BOND STATUS**

	Allocated	Spent	Remaining
Series 2013	\$425,936	\$401,536	\$24,399
Series 2014	\$1,484,064	\$1,525,479	\$(41,415)



### **UPCOMING MILESTONES**

Project Status Close Out

- Construction is nearing completion and the street is open for use.
- Open for use.



# **Columbus Avenue Streetscape Project**

### **BOND STATUS**

	Allocated	Spent	Remaining
Series 2014	\$1,059,524	\$644,450	\$415,074



#### **UPCOMING MILESTONES**



Close Out

- Construction was completed at the end of 2017.
- Open for use.



### **Excelsior and South Bernal Areawides Project**

### **BOND STATUS**

	Allocated	Spent	Remaining	
Series 2013	\$328,627	\$231,024	\$97,603	
				100



### **UPCOMING MILESTONES**

Project Status

Close Out

- Construction is substantially complete.
- Closeout is in progress.
- Open for use.



## **Gough Street Pedestrian Improvements**

### **BOND STATUS**

	Allocated	Spent	Remaining
Series 2013	\$427,587	\$405,092	\$22,495



### **UPCOMING MILESTONES**

### Project Status Close Out


- Construction is complete.
- Working with San Francisco Public Works to complete contract closeout.
- Open for use.



### **Masonic Avenue Streetscape**

### **BOND STATUS**

	Allocated	Spent	Remaining
Series 2013	\$5,726,171	\$5,845,433	\$(130,663)
Series 2014	\$13,746,693	\$8,489,880	\$5,256,813



#### **UPCOMING MILESTONES**

#### **Project Status**

Close Out

- Project nearing completion.
- Open for use.



# **Mission Valencia Raised Cycletrack**

### **BOND STATUS**

	Allocated	Spent	Remaining
Series	\$147,189	\$139,600	\$7,589
2014			



#### **UPCOMING MILESTONES**

#### **Project Status**

Close Out

- Construction is complete.
- Open for use.



### Pedestrian Countdown Signals Design and Construction

### **BOND STATUS**

	Allocated	Spent	Remainin g	
Series 2012B	-	-	-	A Los and a los
Series 2013	\$500,000	504,639	\$(4,639)	
Series 2014	\$2,000,000	\$1,842,921	\$157,079	



### **UPCOMING MILESTONES**

Key Milestone	Forecast Date
Substantial Completion	Winter 2018

- Construction complete at most locations.
- Construction is 98% complete.



# **Polk Streetscape**

### **BOND STATUS**

	Allocated	Spent	Remainin g
Series 2012B	-	-	-
Series 2013	-	-	-
Series 2014	\$2,711,399	\$1,810,692	\$900,708





### **UPCOMING MILESTONES**

Key Milestone	Forecast Date
Substantial Completion	Winter 2019

- Bay to Jackson is paved and restriped.
- Street light underground work continues between Ellis and Post.



### Safe Routes to School Projects Tenderloin

### **BOND STATUS**

	Allocate d	Spent	Remaining
Series 2013	\$287,922	\$275,266	\$12,656
Series 2014	\$163,099	\$178,945	\$(15,846)



### **UPCOMING MILESTONES**



- Construction is complete.
- Open for use.



### **Traffic Calming Improvements Area Wide**

### **BOND STATUS**

	Allocated	Spent	Remaining
Series 2012B	-	-	-
Series 2013	\$777,700	\$780,766	\$(3,066)
Series 2014	-	-	-



### **UPCOMING MILESTONES**

### Project Status

Close Out

- Construction is complete.
- Open for use.



### **Traffic Calming Program Implementation** (application-based program)

#### **BOND STATUS**

	Allocated	Spent	Remaining
Series 2012B	-	-	-
Series 2013	-	-	-
Series 2014	\$912,725	\$730,234	\$182,491



**UPCOMING MILESTONES** 

Project Status

Close Out

- Construction is complete.
- Open for use.



# **Questions?**



