VANNESS IMPROVEMENT PROJECT

Van Ness BRT CAC September 24









UNION









For those calling in, please mute your phones when not speaking.

- 1. Call to order.
- 2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
- 3. Approval of Minutes.
 - a. June 25
- 4. SFMTA staff updates.
- 5. Member comment.
- 6. Adjourn.

CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.


Public Comment

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes


• June 25

Project Schedule

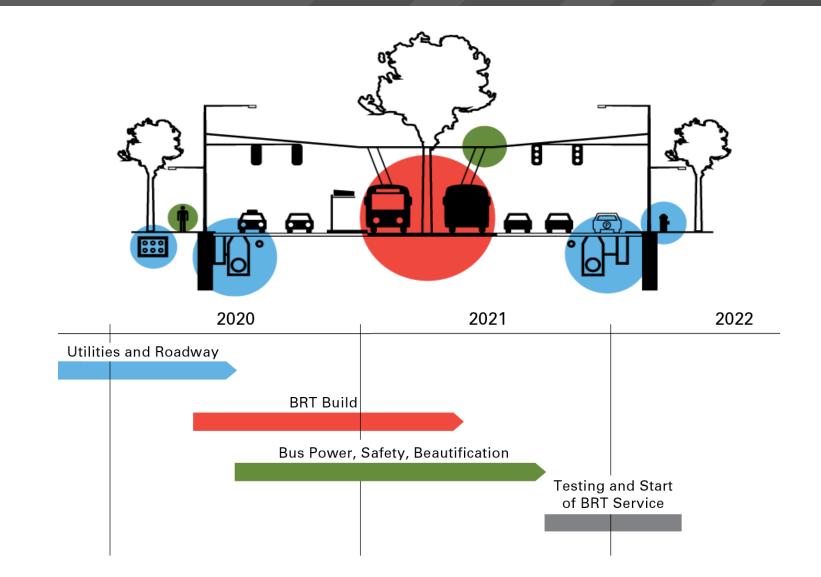


Project Schedule

Phases 1A and 1B almost complete.



Phases 1C and 1D almost complete.




Start		Finish	
1A	Fall 2016	Fall 2020*	
1B	Summer 2018	Summer 2020*	
1C	Summer 2019	Fall 2020*	
1D	Fall 2019	Winter 2021*	
2	Summer 2020*	Fall 2021*	
3	Fall 2020*	Fall 2021*	

*Estimated

٠

Project Schedule

• Phase 2 in progress.

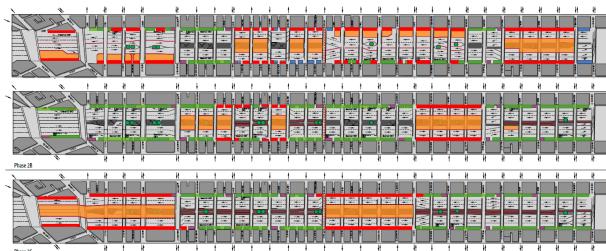

Start Finish 1A Fall 2016 Fall 2020* 1B Summer Summer 2018 2020* 1C Summer Fall 2020* 2019 Fall 2019 Winter 1D 2021* 2 Summer Fall 2021* 2020* Fall 2021* 3 Fall 2020*

• Phase 3 in progress.



*Estimated

	Joint Trench %	Sewer %	Water %	Roadway %	Sidewalk %
1A*	100%	100%	100%	100%	87%
1B*	100%	100%	100%	86%	33%
1C*	99%	100%	100%	76%	70%
1D*	99%	100%	100%	15%	14%

Construction is approximately at 57% completion based on expenditures

Construction update

- Wrapping up Utilities Phase
 - Completed utilities work includes:
 - Sewer work 20,035 LF
 - Water work 24,438 LF
 - Alternate Water Service System (AWSS)
 - Electrical duct bank 11,995 LF

BRT Buildout Phase has begun

- Construction in middle of the roadway
- Construction of red transit-only lanes, median islands, landscaping, bus shelters, bulb-outs, pole setting installations

- Directed Business Support Program launched
 - Provides free one-on-one business consulting services and resources to merchants in the impact zone
 - Joint initiative between OEWD, San Francisco Small Business
 Development Center (SBDC) and SFMTA
 - Application period now open, deadline is October 31, 2020
 - Funding of \$5,000-\$10,000 available to eligible businesses
 - Within the Van Ness construction impact zone
 - Active storefront business
 - Established with no change in ownership on or prior to March 3, 2017
 - Applications are available at www.oewd.org/construction-mitigation

Geary Rapid Project

As part of the <u>Geary Rapid Project</u>, work to replace aging water and sewer lines between Masonic Street and Van Ness Avenue, in coordination with the San Francisco Public Utilities Commission, continues. Transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, have also started and are being managed by San Francisco Public Works.

For more information visit SFMTA.com/Geary or contact GearyRapid@SFMTA.com

Neighboring Project Updates

Lombard Street Vision Zero Project

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

- General working hours: Monday through Friday, 7:00 a.m. to 3:00 p.m.
- Project completion scheduled June 2020. CalTrans to repave the roadway at a later date.

For more information visit SFPublicWorks.org/Lombard or call 415-558-5282

- Outreach Updates
 - Recent Activities
 - Canvassing for Directed Business Support program

Member Comment

 Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

Next Meeting




November 26, 6:00 p.m.

Thank You



VAN NESS











G**F** Caltrans



Water Power Sewer

