

VAN NESS

IMPROVEMENT PROJECT



Van Ness BAC
June 20



Agenda

1. Call to order. Van Ness Business Advisory Committee members please sit at table.
2. Public comment for matters within BAC jurisdiction not on today's calendar.
3. Approval of Minutes – May 16.
4. Presentation and discussion by San Francisco Police Department on patrols along Van Ness Avenue.
5. SFMTA staff updates.
6. Next meeting.

BAC administration reminder

- BAC members are asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

Public Comment

- See Public Comment Policy on back of agenda.
- Public comment for matters that are within the Van Ness Business Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes


- May 16.

SFPD Presentation

- Discussion of patrols on Van Ness Avenue with SFPD



Staff updates

- Project update


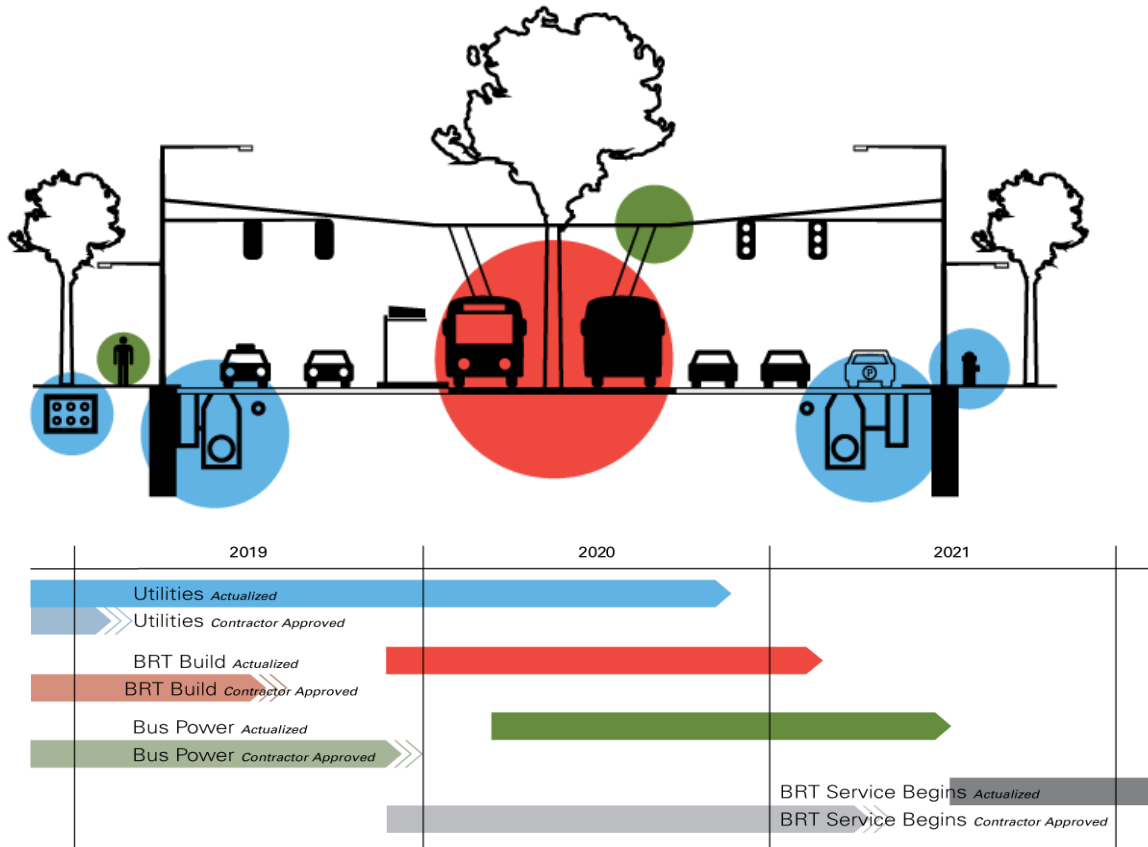


Staff Updates

- Phases 1A and 1B underway. Expected completion summer 2019



- Phases 1C and 1D scheduled spring 2019-spring 2020




	Start	Finish
1A	Fall 2016	Summer 2019*
1B	Summer 2018	Winter 2019*
1C	Summer 2019*	Spring 2020*
1D	Winter 2019*	Summer 2020*
2	Winter 2019*	Spring 2021*
3	Summer 2020*	Summer 2021*

*Estimated

Staff Updates

- Phase 2 scheduled winter 2020-winter 2021

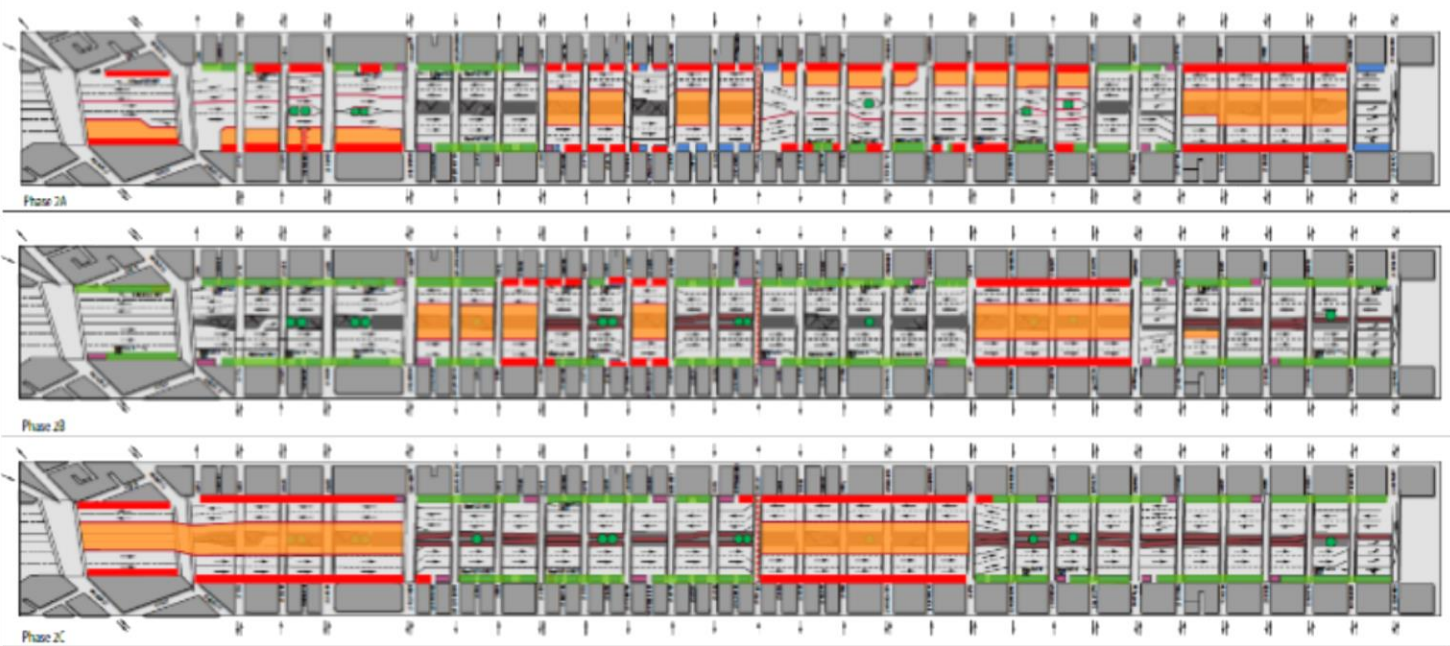

	Start	Finish
1A	Fall 2016	Summer 2019*
1B	Summer 2018	Winter 2019*
1C	Summer 2019*	Spring 2020*
1D	Winter 2019*	Summer 2020*
2	Winter 2019*	Spring 2021*
3	Summer 2020*	Summer 2021*

*Estimated

- Phase 3 scheduled spring 2020-spring 2021



Staff Updates

Traffic and utility zones shifting

- Started night of Wednesday, June 19
- Continues utility work on opposite side of Van Ness
- Utility work is halfway complete
- Traffic lane and construction zone adjustment will take place over 4 weeks
- Meters will be removed
- Loading and blue zones for parking with a valid disabled permit will be relocated. Map of specific locations of relocated colored curb zones can be found at SFMTA.com/VanNess
- Construction fencing will be installed around new work zones

Staff Updates

Project contract modification to MTA Board

- Tuesday, July 16, 1:00 p.m. City Hall, Room 400
- Aims to resolve two contractor claims for unavoidable delays resulting from water and sewer issues
- Covered by project's allocated allowances, does not increase project budget
 - SFPUC provided analysis and agrees to resolution
 - Increases the contract amount by \$4,819,650
 - Increases contract duration by 279 total calendar days
 - Of claimed 279 days unavoidable delays, 135 days are justifiable due to sewer and water issues
 - Contractor agrees to drop remaining 144 delay days claims and to avoid any litigation cost for both parties

Staff Updates

Construction update

- Construction is approximately at 34% completion (33% in May)
- Traffic lane and construction zone shifts underway
- Joint trenching ongoing
- Addressing utility conflicts
- Sidewalk replacement, street base repair and paving work – outreach to affected blocks ongoing
- SFPD additional nighttime patrols and increased enforcement of construction zones



Staff Updates

Geary Rapid Project

The first phase of construction as part of the [Geary Rapid Project](#) continues. Work to replace aging water and sewer lines between Masonic Street and Van Ness Avenue is scheduled to be done in coordination with the San Francisco Public Utilities Commission (SFPUC).

Water main replacement work is planned for the week of June 17 near Scott Street. Sewer main replacement is scheduled for the week of June 17 between Presidio and Scott streets. Additionally, there will be testing of newly installed water pipes on the weeks of June 17.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Staff Updates

Lombard Street Vision Zero Project

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

Crews are scheduled to install new curb ramps and sidewalk at Richardson Avenue and Francisco and Chestnut street intersections. On the north side of Lombard Street from Webster Street to Richardson Avenue, crews are scheduled to continue with sewer work.

General working hours Monday through Friday 7:00 a.m. to 3:00 p.m.

For more information visit SFPublicWorks.org/Lombard or call 415-558-5282

Staff Updates

- Outreach Updates

- SFCTA Citizens Advisory Committee, May 22
- Community Living Campaign's Van Ness Street Safety Search Party, May 23
- Van Ness BRT Community Advisory Committee, May 23
- Meet the Expert, June 5 at Rangoon Ruby
- Distribution of Van Ness Improvement Project newsletter via mail to ~30k project neighbors
- Business Support Car Card installation
- Traffic and Construction Zone shift outreach
 - Doorhangers
 - Press release
 - Blog

Staff Updates

- Outreach Updates
 - Upcoming outreach activities
 - Van Ness BRT Community Advisory Committee Meeting
 - June 27, 5:00 p.m.
 - 1 South Van Ness, Union Square Conference Room, 7th Floor
 - Block meetings for blocks where construction zone is moving
 - Meet the Expert: August 7, 6:00 p.m.

Next Meeting



August 15, 3:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess

