#### VANNESS IMPROVEMENT PROJECT

### Van Ness BRT CAC June 27

















For those calling in, please mute your phones when not speaking by dialing \*6. Unmute to speak by dialing \*6 again.

- 1. Call to order. Van Ness BRT Community Advisory Committee members please sit at table.
- 2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
- 3. Approval of Minutes May 23.
- 4. SFMTA staff updates.
- 5. Member comment.
- 6. Adjourn.

## CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum
- If no quorum can be reached, meeting to be canceled


## Public Comment

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.


## Approval of Minutes


• May 23.

• Project update

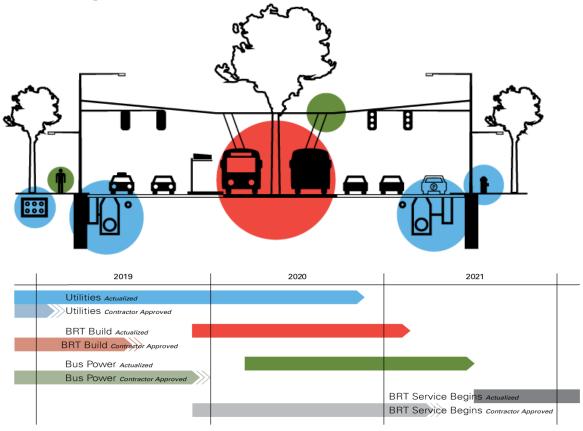


Phases 1A and 1B underway. Expected completion summer 2019






\*Estimated


• Phases 1C and 1D scheduled spring 2019-spring 2020



• Phase 2 scheduled winter 2020-winter 2021

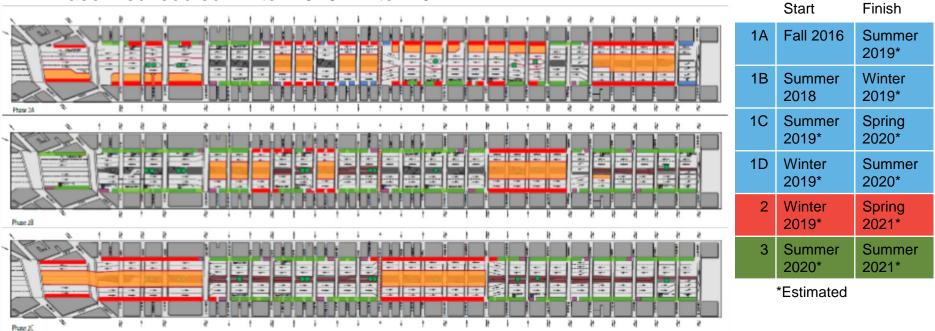

• Phase 3 scheduled spring 2020-spring 2021



Traffic and utility zones shifting

- Started night of Wednesday, June 19
- Continues second half of utility work on opposite side of Van Ness
- Traffic lane and construction zone adjustment will take
  place over several weeks
- Meters will be removed
- Loading and blue zones for parking with a valid disabled permit will be relocated. Map of specific locations of relocated colored curb zones can be found at SFMTA.com/VanNess
- Construction fencing will be installed around new work zones

Project contract modification to MTA Board

- Tuesday, July 16, 1:00 p.m. City Hall, Room 400
- Aims to resolve two contractor claims for unavoidable delays resulting from water and sewer issues
- Covered by project's allocated allowances, does not increase project budget
  - SFPUC provided analysis and agrees to resolution
    - Increases the contract amount by \$4,819,650
    - Increases contract duration by 279 total calendar days
      - Of claimed 279 days unavoidable delays, 135 days are justifiable due to sewer and water issues
    - Contractor agrees to drop remaining 144 delay days claims and to avoid any litigation cost for both parties

#### Construction update

- Construction is approximately at 34% completion (33% in May)
- Traffic lane and construction zone shifts underway
- Joint trenching ongoing
- Addressing utility conflicts
- Sidewalk replacement, street base repair and paving work outreach to affected blocks ongoing
- SFPD additional nighttime patrols and increased enforcement of construction zones



#### **Geary Rapid Project**

- Water main replacement work planned for the weeks of June 24 and July 1 near Scott Street.
- Testing of newly installed water pipes planned for the week of June 24 between Presidio and Scott streets.
- Sewer main replacement is planned for the week of June 24 and July 1 on Geary Boulevard between Divisadero and Scott streets.

For more information visit SFMTA.com/Geary or contact GearyRapid@SFMTA.com

#### Lombard Street Vision Zero Project

- Crews are scheduled to install new curb ramps and sidewalk at Richardson Avenue and Francisco and Chestnut street intersections.
- Crews scheduled to continue with sewer work on the north side of Lombard Street from Webster Street to Richardson Avenue.
- Night work is planned on Lombard Street from Laguna Street to Richardson Avenue.

For more information please visit sfpublicworks.org/Lombard.

- Outreach Updates
  - Recent outreach activities
    - Meet the Expert, June 5 at Rangoon Ruby
    - Van Ness Business Advisory Committee Meeting, June 20
    - Distribution of Van Ness Improvement Project newsletter via mail to ~30k project neighbors
    - Business Support Car Card installation
    - Traffic and Construction Zone shift outreach
      - Doorhangers
      - Press release
      - Blog



- Outreach Updates
  - Upcoming outreach activities
    - Van Ness Business Advisory Committee Meeting
      - July 18, 3:00 p.m.
      - 1 South Van Ness, Civic Center Conference Room, 3rd Floor
    - Block meetings for blocks where construction zone is moving
    - Meet the Expert: August 7, 6:00 p.m.

## Member Comment

 Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

## Next Meeting



August 22, 6:00 p.m.

## Thank You



# VAN NESS











Est for the second seco





