

# VAN NESS

# IMPROVEMENT PROJECT



## *Van Ness BRT CAC*

*February 25*



# Agenda

***For those calling in, please mute your phones when not speaking.***

1. Call to order.
2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
3. Approval of Minutes.
  - a. [January 28, 2021](#)
4. SFMTA staff updates.
5. Member comment.
6. Adjourn.

# *CAC administration reminder*

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.


# *Public Comment*

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

# *Approval of Minutes*


- January 28, 2021

# Project Schedule

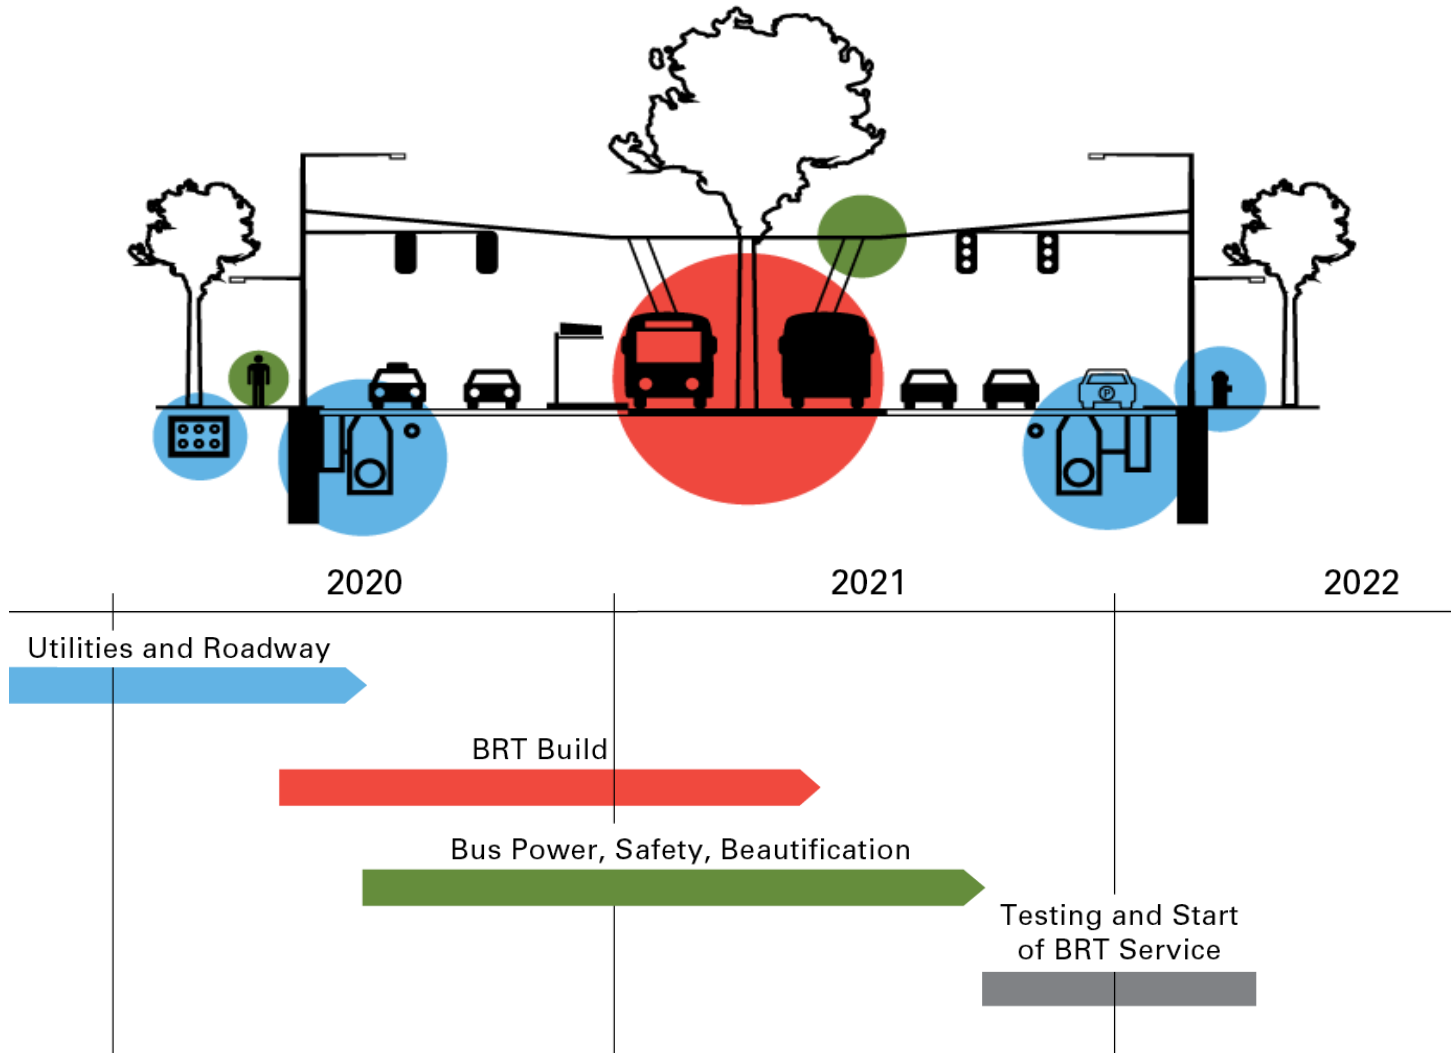


# Project Schedule

- Phases 1A and 1B almost complete.





Phase 1A



Phase 1B

- Phases 1C and 1D almost complete.




Phase 1D

	Start	Finish
1A	Fall 2016	Winter 2021*
1B	Summer 2018	Summer 2021*
1C	Summer 2019	Summer 2021*
1D	Fall 2019	Fall 2021*
2	Summer 2020	Fall 2021*
3	Spring 2021*	Fall 2021*

\*Estimated

# Project Schedule

- Phase 2 underway. Expected completion fall 2021.

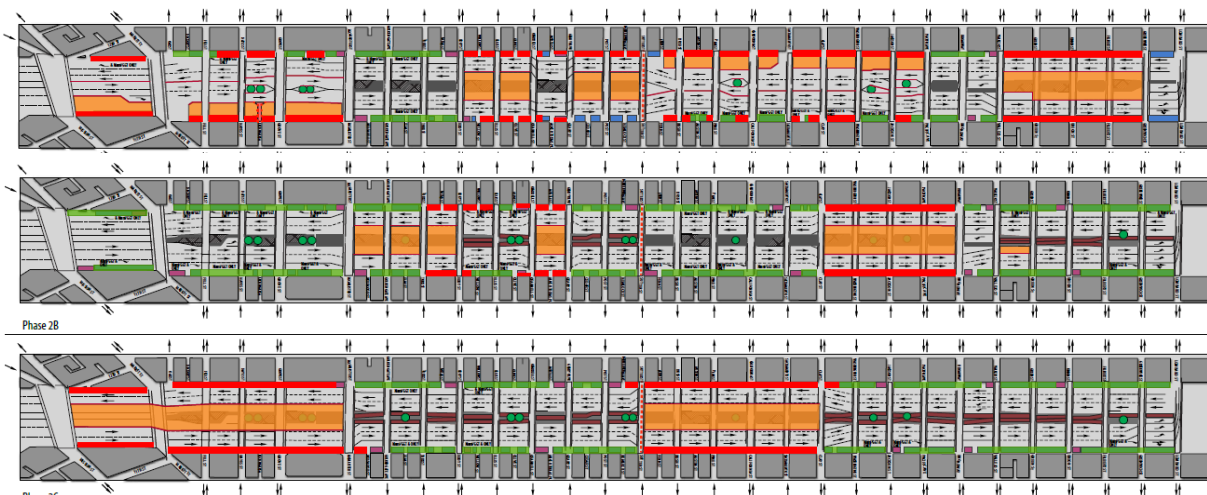

- Phase 3 underway. Expected completion fall 2021.



	Start	Finish
1A	Fall 2016	Winter 2021*
1B	Summer 2018	Summer 2021*
1C	Summer 2019	Summer 2021*
1D	Fall 2019	Fall 2021*
2	Summer 2020	Fall 2021*
3	Spring 2021*	Fall 2021*

\*Estimated



# Staff Updates

	Utilities%	Roadway %	Sidewalk %
1A*	100%	100%	87%
1B*	100%	86%	60%
1C*	100%	82%	73%
1D*	100%	54%	40%

- Construction is approximately at 66.28% completion based on expenditures

# Staff Updates

## Construction update

- BRT Buildout Phase in progress
  - Construction of median islands, bus shelters, bulb-outs
  - Installation of red transit lanes, pole setting



# *Staff Updates*

- Corridor marketing plan being presented to Business Advisory Committee

# Staff Updates

## Geary Rapid Project

As part of the [Geary Rapid Project](#), work to replace aging water lines, in coordination with San Francisco Public Utilities Commission, continues. Surface transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, are also underway and are being managed by San Francisco Public Works.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact [GearyRapid@SFMTA.com](mailto:GearyRapid@SFMTA.com)

# Neighboring Project Updates

## Lombard Street Vision Zero Project


The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

- General working hours: Monday through Friday, 7:00 a.m. to 3:00 p.m.
- Project completed, with Caltrans to repave the roadway soon.

For more information visit [SFPublicWorks.org/Lombard](https://SFPublicWorks.org/Lombard) or call 415-558-5282

# Staff Updates

- Outreach Updates
  - Recent outreach activities
    - Winter newsletter sent by email
    - SFMTA Van Ness BAC meeting February 18
  - Upcoming outreach activities
    - Spring newsletter to be sent by mail

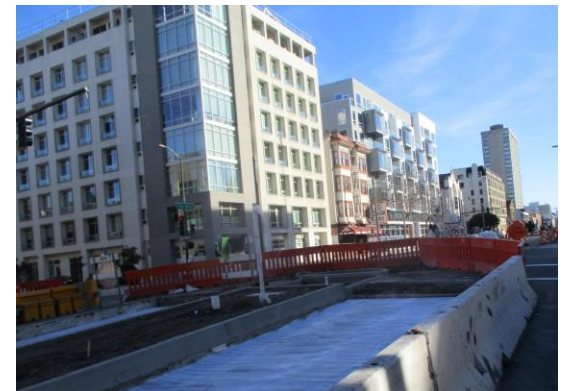

# *Member Comment*

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

# *Next Meeting*



April 22, 6:00 p.m.



# Thank You



## VAN NESS



[SFMTA.com/VanNess](http://SFMTA.com/VanNess)



San Francisco  
Water  
Power  
Sewer

