

VAN NESS

IMPROVEMENT PROJECT



Van Ness BRT CAC

October 28, 2021



Agenda

For those calling in, please mute your phones when not speaking.

1. Call to Order.
2. Public comment: Members of the public may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar
3. Approval of minutes – [September 23, 2021](#).
4. Presentation, discussion and possible action regarding update from SFMTA staff.
 - Project Schedule.
 - Construction update.
 - Update on neighboring projects.
 - Outreach update.
5. Member comment: Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar
6. Adjourn

CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

Public Comment


- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes

- September 23, 2021

Staff updates

- Project schedule

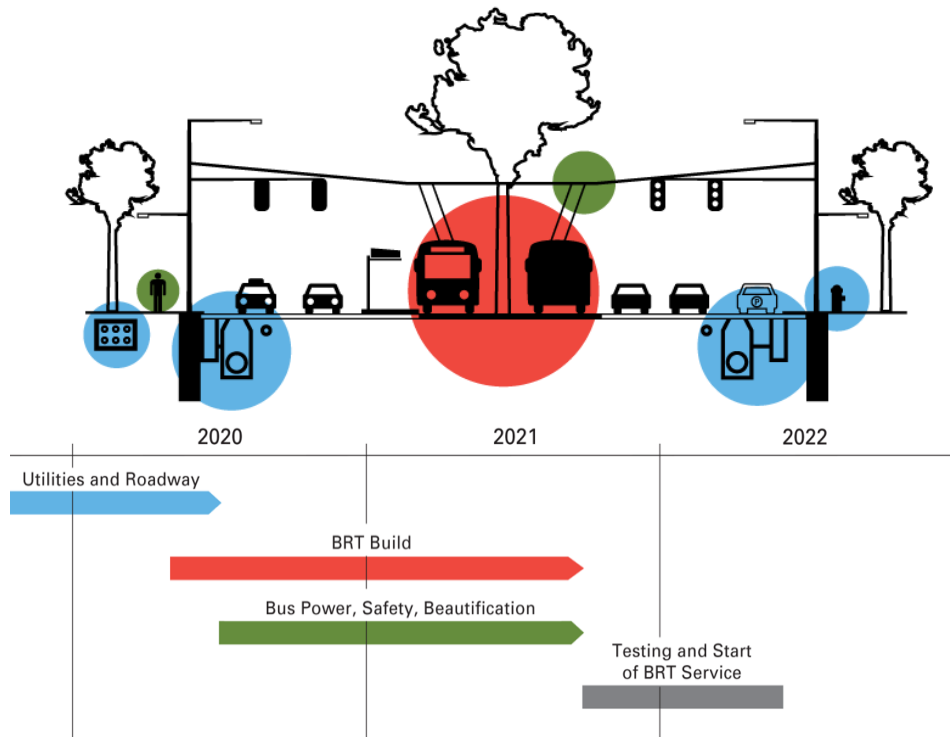

Start	Finish
Fall 2016	Winter 2022
Summer 2020	Fall 2021
Spring 2021	Summer 2021 to Fall 2021

Staff Updates

	Utilities%	Roadway %	Sidewalk %
1A*	100%	100%	95%
1B*	100%	95%	90%
1C*	100%	95%	90%
1D*	100%	95%	90%

- As of September: Construction is approximately at 88.1% completion based on expenditures (September was 86.47%)

Staff Updates

Construction update

Current work

- ~95% of the bulb out work is complete
- Irrigation and backfill work ongoing in the median
- All traffic signals except Lombard have been cutover to the new signal boxes
- Tree planting at the sidewalk is progressing towards Mission; median trees to follow

Staff Updates

Outreach Updates

- Fall 2021 quarterly newsletter forthcoming
- Currently planning for opening ceremony early Spring 2022

Staff Updates

Geary Rapid Project

Construction work on the [Geary Rapid Project](#), in coordination with San Francisco Public Utilities Commission and San Francisco Public Works, is nearly complete. Installation of red transit lane treatments is underway. All other contract work is complete, including 1.5 miles of new sewer, almost three miles of upgraded water mains, 1.5 miles of roadway repaving, three new and eight upgraded traffic signals, four new pedestrian crossings, 32 pedestrian bulb-outs, 12 transit bulb-outs and 38 upgraded curb ramps.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Member Comment

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

Next Meeting



February 24, 6:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess

