

# VAN NESS

# IMPROVEMENT PROJECT

*Van Ness BAC*  
*March 21*



# *Agenda*

1. Call to order. Van Ness Business Advisory Committee members please sit at table.
2. Public comment for matters within BAC jurisdiction not on today's calendar.
3. Approval of Minutes – December 20.
4. Presentation, discussion and possible action regarding proposed art.
5. SFMTA staff updates.
6. Next meeting.

# *BAC administration reminder*

- BAC members are asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

# *Public Comment*


- See Public Comment Policy on back of agenda.
- Public comment for matters that are within the Van Ness Business Advisory Committee jurisdiction and are not on today's calendar.

# *Approval of Minutes*

- December 20.

# Staff Updates



- Project schedule

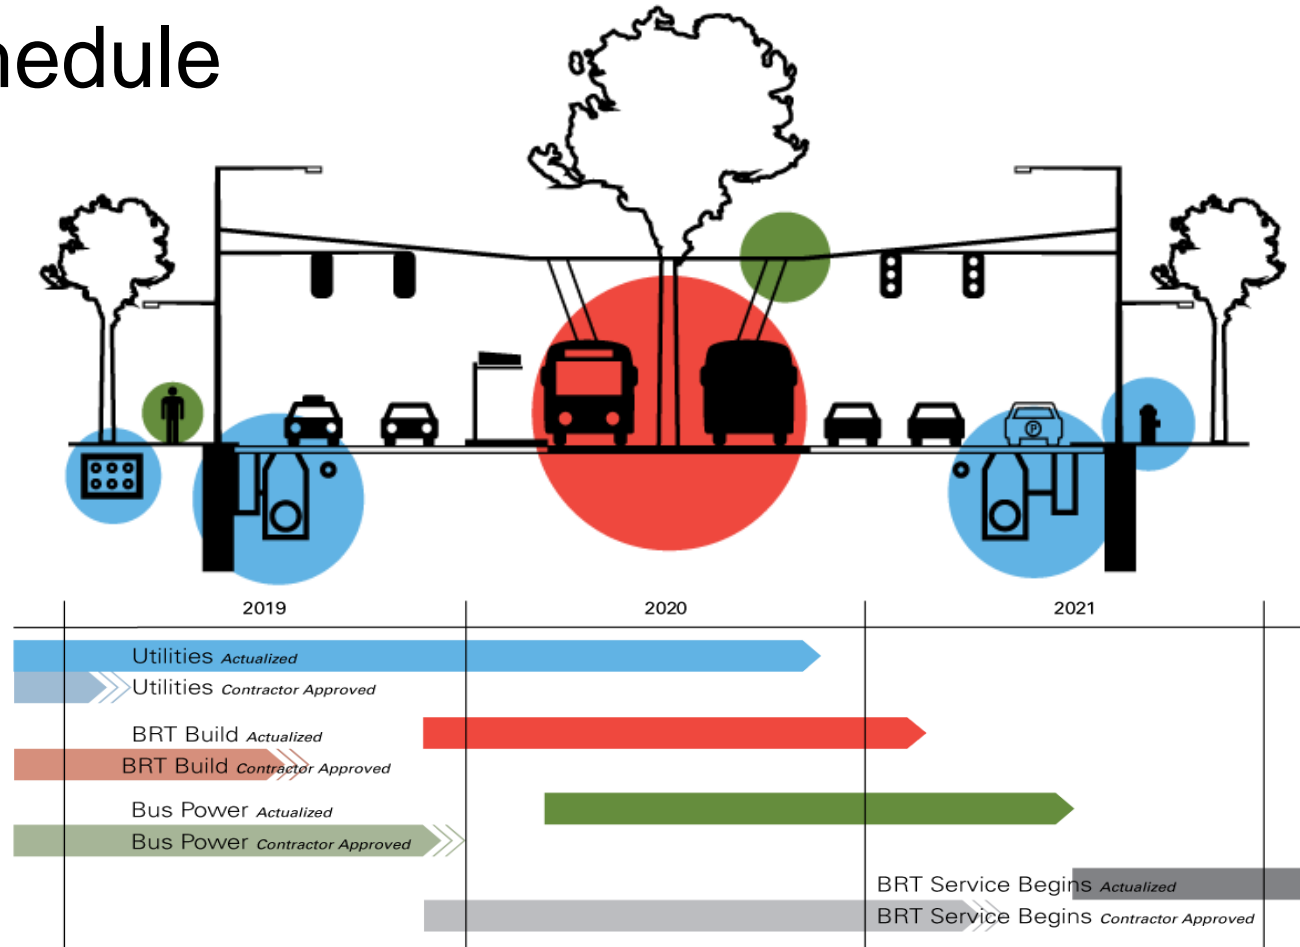



# Staff Updates



- Phases 1A and 1B underway. Expected completion summer 2019



	Start	Finish
1A	Fall 2016	Winter 2019*
1B	Summer 2018	Summer 2019*
1C	Spring 2019*	Summer 2020*
1D	Summer 2019*	Spring 2020*
2	Winter 2020*	Winter 2021*
3	Spring 2020*	Spring 2021*


\*Estimated

- Phases 1C and 1D scheduled spring 2019-spring 2020



# Staff Updates


- Phase 2 scheduled winter 2020-winter 2021

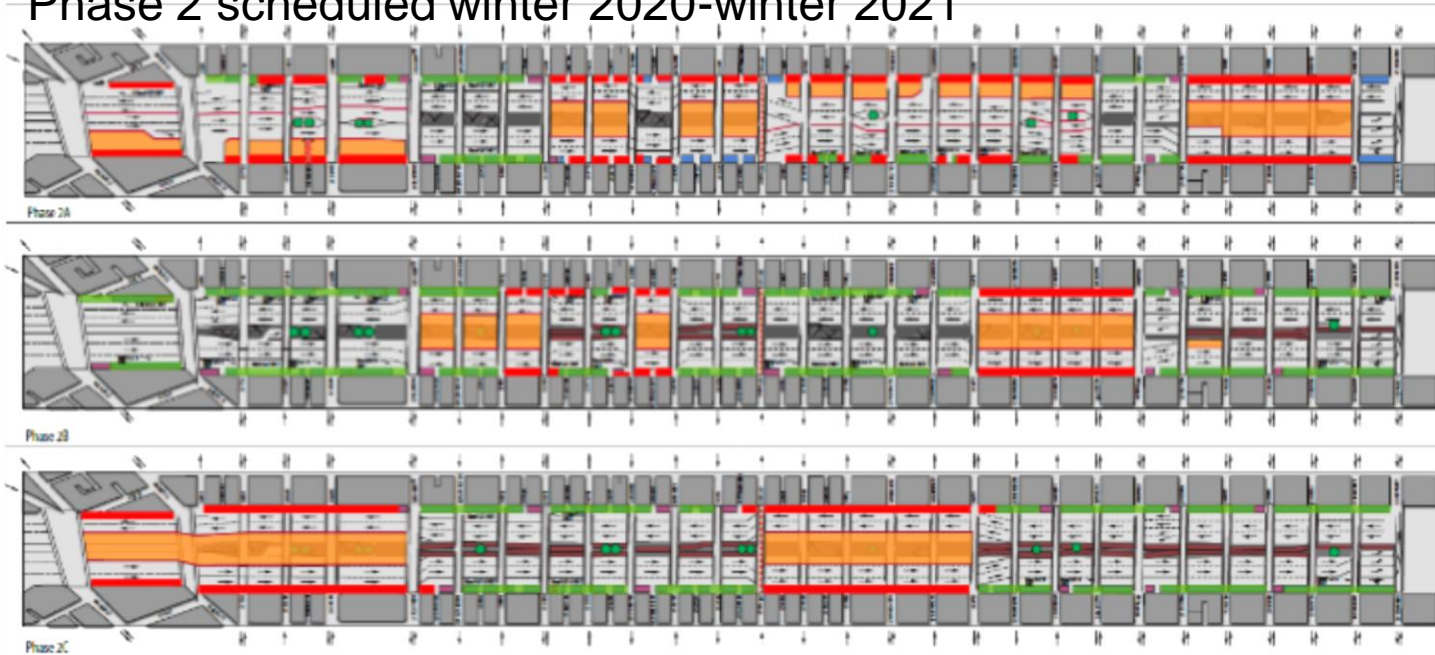

	Start	Finish
1A	Fall 2016	Winter 2019*
1B	Summer 2018	Summer 2019*
1C	Spring 2019*	Summer 2020*
1D	Summer 2019*	Spring 2020*
2	Winter 2020*	Winter 2021*
3	Spring 2020*	Spring 2021*

\*Estimated

- Phase 3 scheduled spring 2020-spring 2021

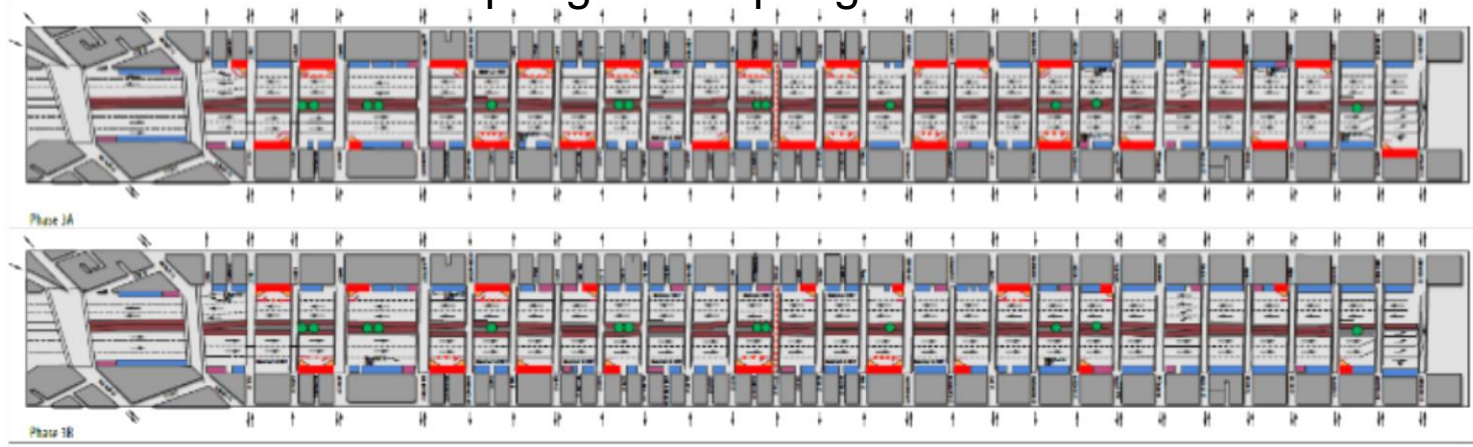



# Staff Updates

## Construction update

- Construction is approximately at 28% completion (27% in January)
- Joint trenching ongoing
- Addressing utility conflicts
- Sewer installation – intensive night work
- Sidewalk replacement work – outreach to affected blocks ongoing
- SFPD additional nighttime foot patrols and increased enforcement of construction zones



# *Staff Updates*

- **Outreach Updates**

- **Recent Milestones**

- SFCTA Citizens Advisory Committee Meeting, February 27
    - Van Ness BRT Community Advisory Committee, February 28
    - Meet the Expert at Alborz Restaurant, March 6
    - Digital Newsletter distributed March 18
    - Transportation Authority Board of Commissioners, March 19

# Staff Updates

- Outreach Updates

- Upcoming outreach activities

- SFCTA Citizens Advisory Committee

- March 27, 6:00 p.m.

- SFCTA, 1455 Market Street, 22<sup>nd</sup> Floor

- Van Ness BRT Community Advisory Committee Meeting

- March 28, 5:00 p.m.

- 1 South Van Ness, Union Square Conference Room, 7<sup>th</sup> Floor

- Recruiting members for Van Ness BRT CAC/ Van Ness BAC – Applications due March 29

- Meet the Expert: April 2, 6:00 p.m.



# Staff Updates

## Polk Streetscape Project

Most construction work for the project has been completed. Crews are wrapping up work and performing final striping changes.

Ribbon cutting and community celebration

Tuesday, April 2, 11:00 a.m.-12:00 p.m.

Entrance at Fern Alley at Polk Street

Find out more at [sfpublicworks.org/polk](https://sfpublicworks.org/polk).



# Staff Updates

## Geary Rapid Project

The first phase of construction as part of the Geary Rapid Project has begun. Work to replace aging water and sewer lines between Masonic and Van Ness avenues is scheduled to be done in coordination with the San Francisco Public Utilities Commission (SFPUC).

Water main replacement work scheduled on eastbound Geary Boulevard between St. Joseph's Avenue and Scott Street. Parking will be temporarily restricted on the south side of Geary Boulevard until work is complete. Inbound bust stop on Geary at Divisadero will be relocated slightly west during water work.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact [GearyRapid@SFMTA.com](mailto:GearyRapid@SFMTA.com)

# Staff Updates

## **Lombard Street Vision Zero Project**

- Pedestrian safety, transit performance, and utility improvements (Lombard Street at Richardson)
- Final paving to be done along Lombard Street
- Crews are scheduled to continue installing new water main working west from Fillmore Street to Richardson Avenue. This work will be performed primarily on the north side of Lombard Street with occasional work that crosses the south side of Lombard at some intersections. This work is expected to continue through April 2019.
- General working hours Monday through Friday 7:00 a.m. to 3:00 p.m.
- For more information visit [SFPublicWorks.org/Lombard](http://SFPublicWorks.org/Lombard) or Call 415-558-5282

# *Next Meeting*



May 16, 3:00 p.m.



# Thank You



## VAN NESS

## IMPROVEMENT PROJECT



[sfmta.com/vanness](https://sfmta.com/vanness)
