

Geary Community Advisory Committee

July 14, 2021

Order of Business

- 1. Call to order
- 2. Virtual meeting etiquette
- 3. Roll call
- 4. Welcome new members, ice-breaker
- 5. Chair election
- 6. Approval of minutes May 12, 2021
- 7. Public comment
- 8. Meeting frequency
- 9. Geary Temporary Emergency Transit Lanes update
- 10. Geary Boulevard Improvement Project update
- 11. Geary Rapid Project update
- 12. Geary Rapid Project Outreach update
- 13. Adjourn

2. Virtual Meeting Etiquette

- Microsoft Teams download for desktop or mobile at: <u>www.microsoft.com/en-us/microsoft-teams/download-app</u>
- Key functions: mute/unmute, raise hand, chat
- Please stay on mute unless called on to speak by Chair





4. Welcome new members, ice-breaker

Welcome to new CAC members (filling seats vacated by Annie Lee and Dina Mendoza)!

- Winston Parsons
- Devi Zinzuvadia

Icebreaker:

Please introduce yourself and your connection to Geary.



- Roles and responsibilities of Chair
- Process overview
- Election



Roles and responsibilities of Chair

- Works with project staff to develop and approve meeting agendas
- Facilitates meetings following Robert's Rules of Order with staff support
- Represents the committee for meetings, events and activities



Process overview

- Request nominations from members
- Candidates have an opportunity to address the committee members about their interest
- Public comment
- Members vote publicly on candidates in order received
- First candidate to receive a majority for each seat is elected



Election

- Request nominations from members
- Candidates have an opportunity to address the committee members about their interest
- Public comment
- Members vote publicly on candidates in order received
- First candidate to receive a majority for each seat is elected



6. Approval of minutes

• May 12, 2021



7. Public comment

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Geary Community Advisory Committee jurisdiction and are not on today's calendar.
- Public comment is limited to two minutes each.



8. Meeting frequency

Continue with bi-monthly meetings 6 times/year? (Jan, Mar, May, July, Sept, Nov)


Or quarterly meetings 4 times/year? (Jan, Apr, July, Oct)





9. Geary Temporary Emergency Transit Lanes update

- <u>Detailed Evaluation</u>
 <u>Report</u> and <u>Score Card</u>
 published in June
- Office Hours held June 30, 2021
- SFMTA Board consideration of permanent approval planned July 20, 2021

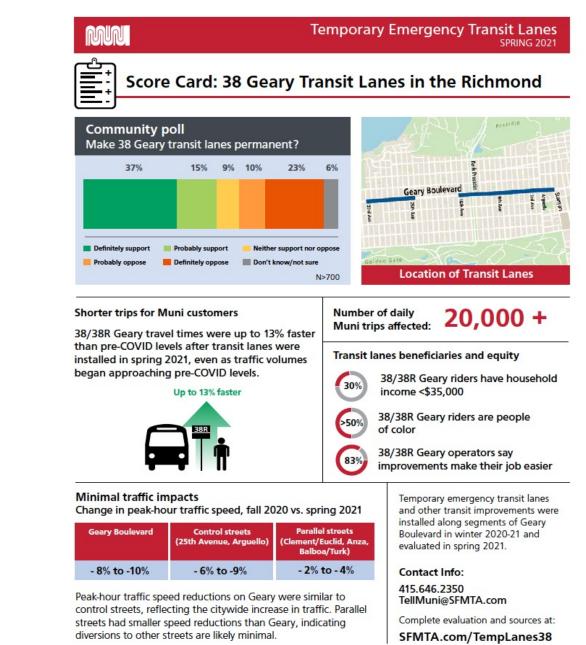

Updates since last meeting

- <u>SF Weekly article</u> (5/27/2021)
- <u>The Frisc blog</u> (6/4/2021)
- <u>Presentation</u> to SFMTA CAC Engineering, Maintenance, and Safety Committee (EMSC) (6/23/2021)




Draft proposed bus stop relocation/removal recommendations

Principles for bus stop re-location:

- 1) Moving bus stops from the nearside of intersections to the farside, so buses don't get stopped at red lights as often
- 2) Removing or consolidating closely-spaced stops to improve travel time reliability
- 3) Expand substandard bus zone lengths



Draft proposed bus stop relocation/removal recommendations

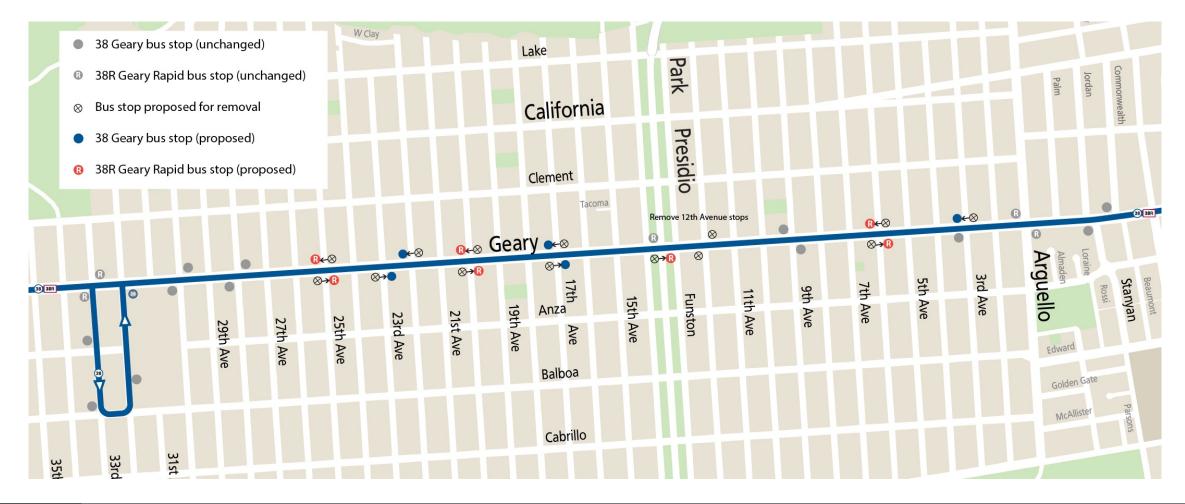

Outreach roadmap

Spring/Summer: Merchant loading survey. Seek input on:

• Loading/access needs to inform development of a curb plan

TBD Fall: Outreach Round 1. Seek input on:

- Level of support for new side-running configuration recommendation
- Proposed bus stop consolidations and removals
- Block-specific feedback on existing transit/parking/loading/ safety challenges to inform draft project design


TBD Fall/Winter: Outreach Round 2. Seek input on:

• Draft block-by-block design

		Design		nstruction	
Budget	\$	5.0M	\$	30.9M	
Expenditures*	\$	4.9M	\$	21.7M	
% expended		99%		70%	
Budget Status		Closing out		On track	
Est. Completion		Summer '19		Sept '21	
Schedule Status		Complete		On track	
		*fina	ncial da	ta as of 6/18/2021	
Geary Rapid Proje					
includes MTA, PUC S	iewer an	d Water, D	r, Pav	ing and Cur	b Ramps
Contract/Work	Est	timated		Price	Status (% paid)
	\$	1.0M	\$	1.0M	Complete
MTA Near-Term	-			16.2M	Complete
MTA Near-Term PUC Sewer/Water	\$	16.0M	\$	10.211	compiete
		16.0M 6.2M	\$ \$	8.7M	Underway (75%)
PUC Sewer/Water	\$		-		
PUC Sewer/Water PW Geary East	\$ \$	6.2M	\$	8.7M	Underway (75%)



Overview

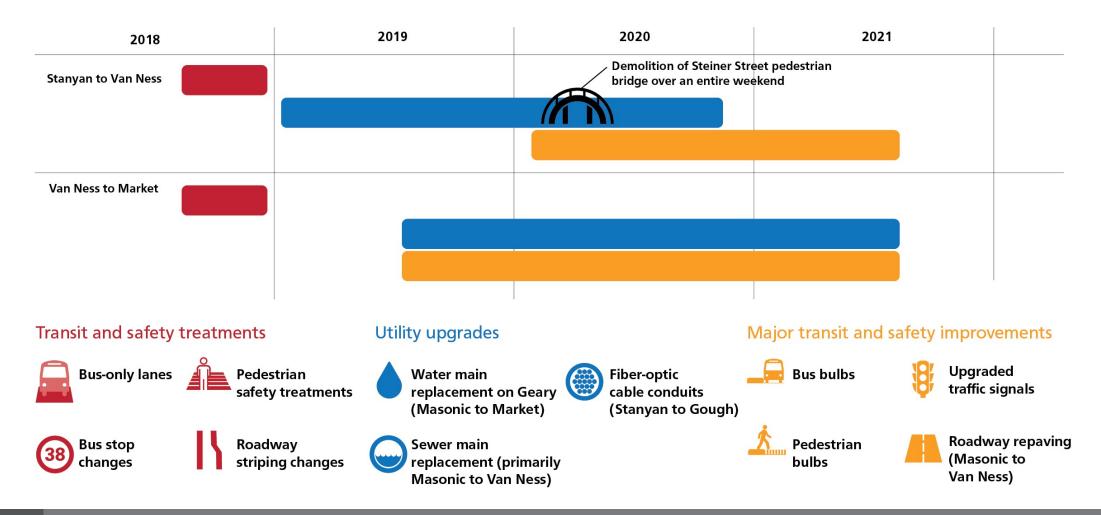

"Geary East" contract: Van Ness to Market Street

- All water mains are installed. Service connection work is underway between Stockton and Kearny streets.
- Sidewalk bulb-out work remaining on Geary at Mason and at Kearny.
- Begin private Verizon conduit work on Geary, pending cost share agreement.



"West Surface" contract: Stanyan to Van Ness

- Work in "Segment A" at Steiner (Hamilton Rec Center) is nearly finished.
- Only work remaining in "Segment B" is the Buchanan crossing as well as railings and median pavers. Tree plantings are planned as well.
- Red thermoplastic is planned to begin west of Van Ness.



12. Geary Rapid Project – Outreach update



Business support: Tenderloin directory

12. Geary Rapid Project – Outreach update



Business support: Tenderloin directory

M

SFMTA

12. Geary Rapid Project – Outreach update

Geary CAC Walking Tour on May 27, 2021





Next meeting:

- September 8, 2021, 6:00 p.m.
- Most likely still virtual on Microsoft Teams, else:

1 South Van Ness Avenue, 7th Floor, Union Square Conference Room

Thank you!

