


# VAN NESS

# IMPROVEMENT PROJECT

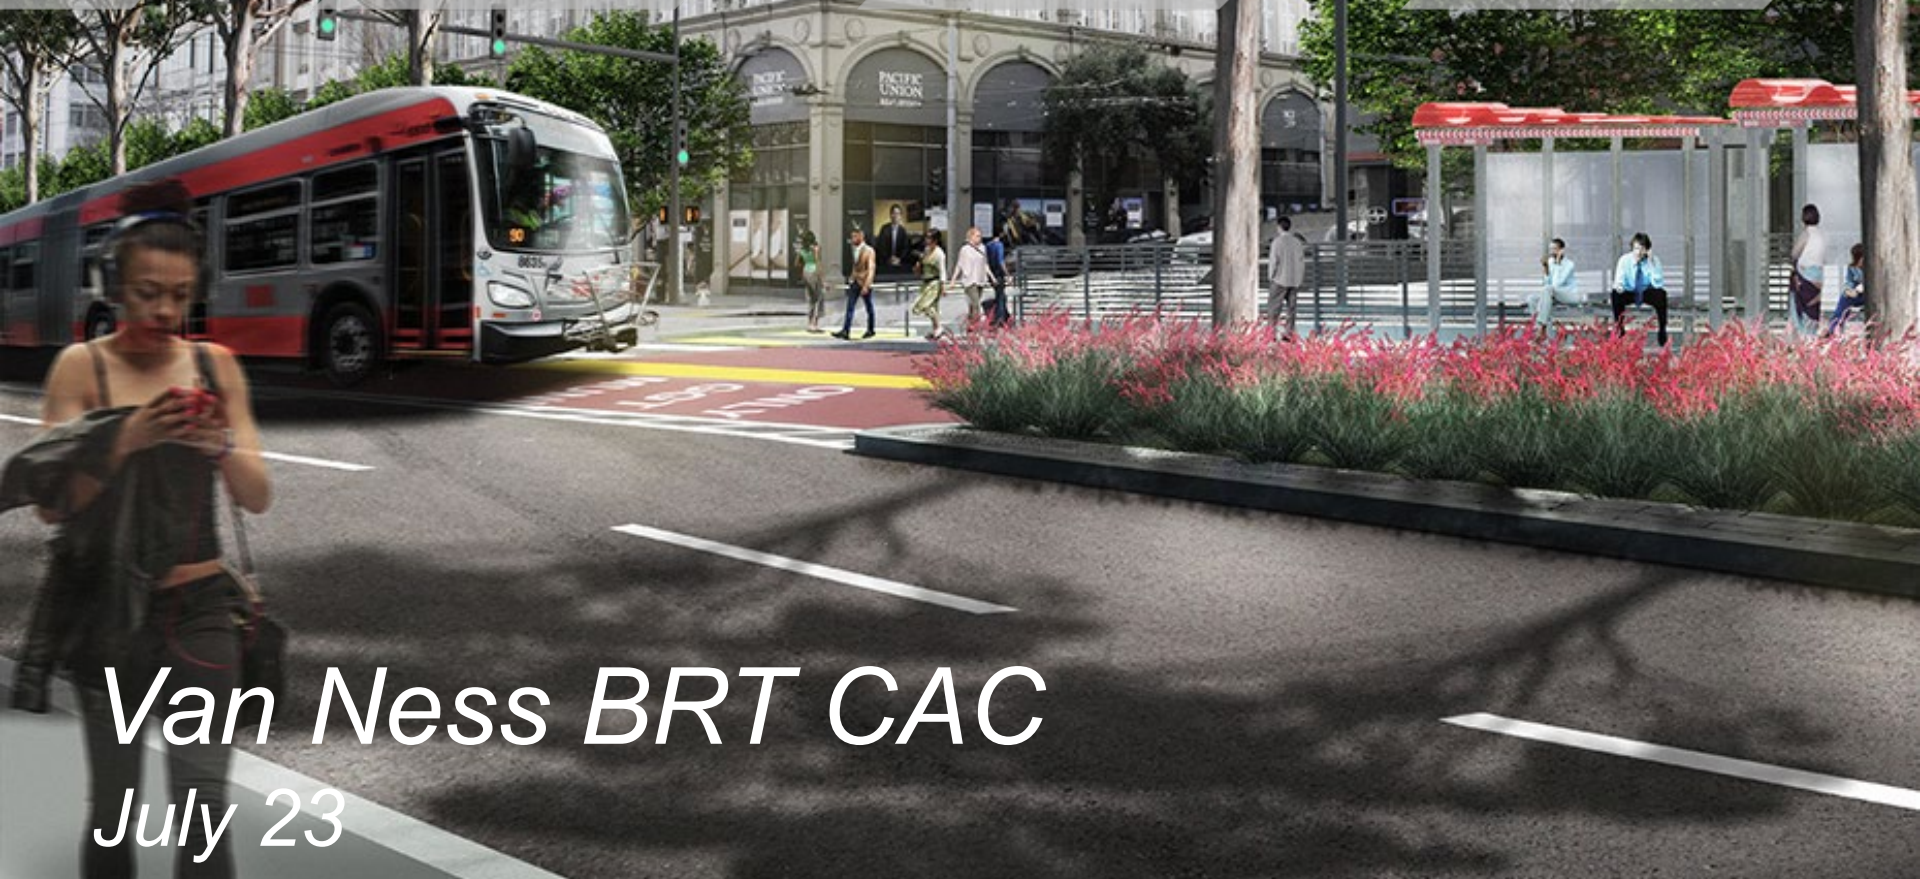

## *Van Ness BRT CAC*

*July 23*



# Agenda

***For those calling in, please mute your phones when not speaking.***

1. Call to order.
2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
3. Approval of Minutes.
  - a. June 25
4. SFMTA staff updates.
5. Member comment.
6. Adjourn.

# *CAC administration reminder*

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.


# *Public Comment*

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

# *Approval of Minutes*



- June 25

# Project Schedule


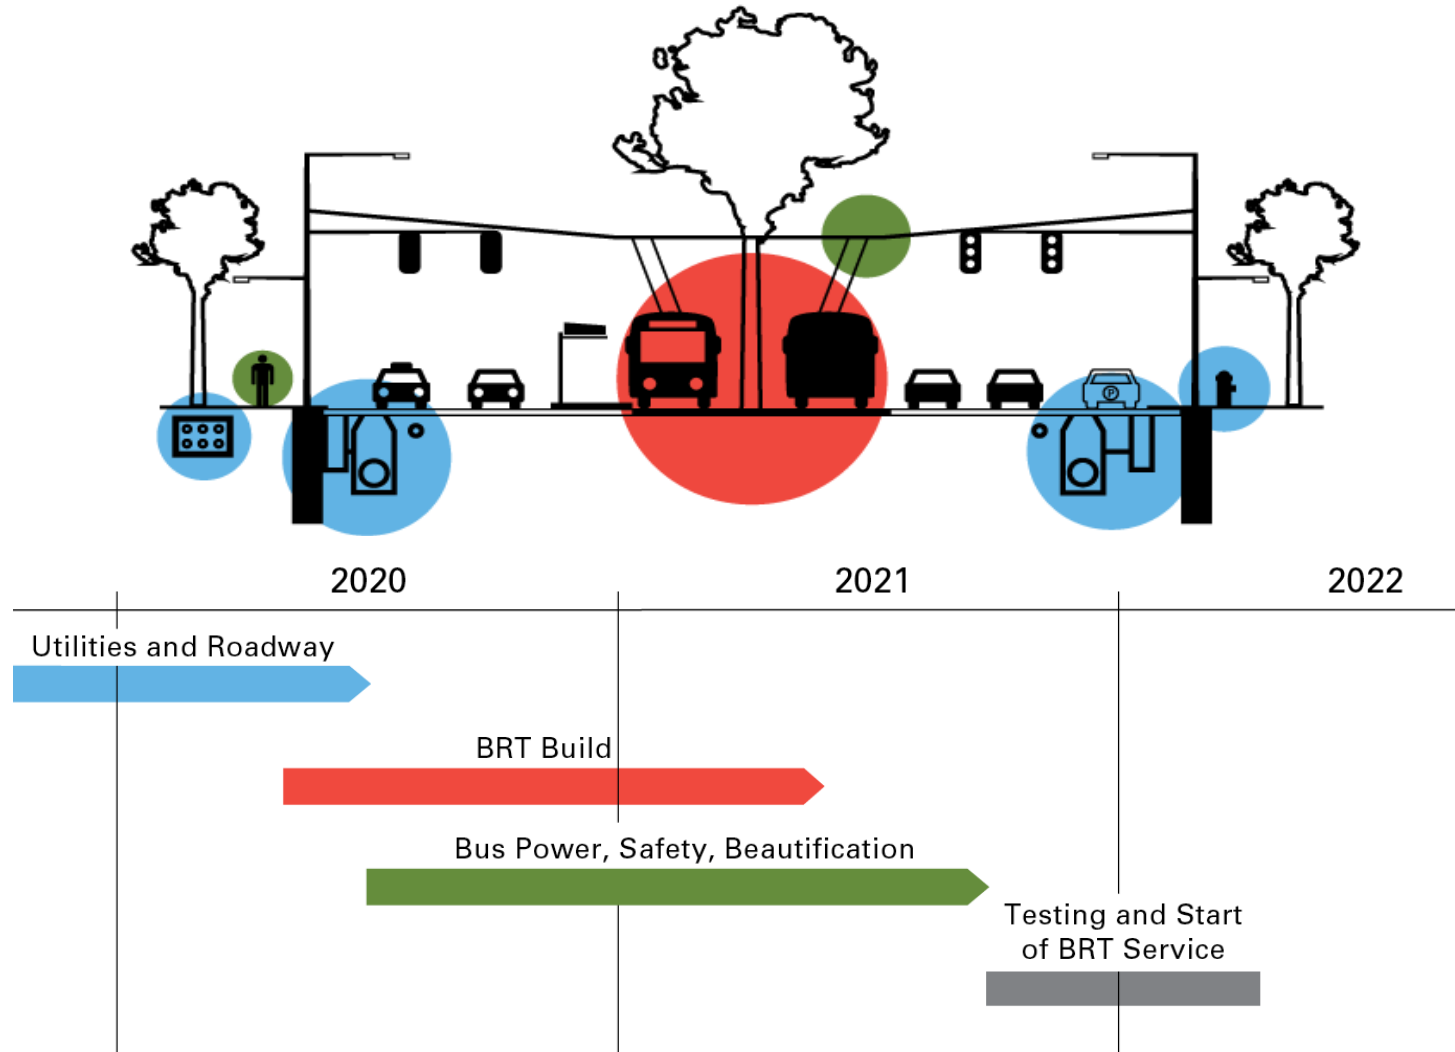


# Project Schedule

- Phases 1A and 1B underway. Expected completion summer 2020



- Phases 1C and 1D underway. Expected completion fall 2020




	Start	Finish
1A	Fall 2016	Summer 2020*
1B	Summer 2018	Summer 2020*
1C	Summer 2019	Fall 2020*
1D	Fall 2019	Fall 2020*
2	Summer 2020*	Fall 2021*
3	Fall 2020*	Fall 2021*

\*Estimated



# Project Schedule

- Phase 2 scheduled summer 2020-fall 2021

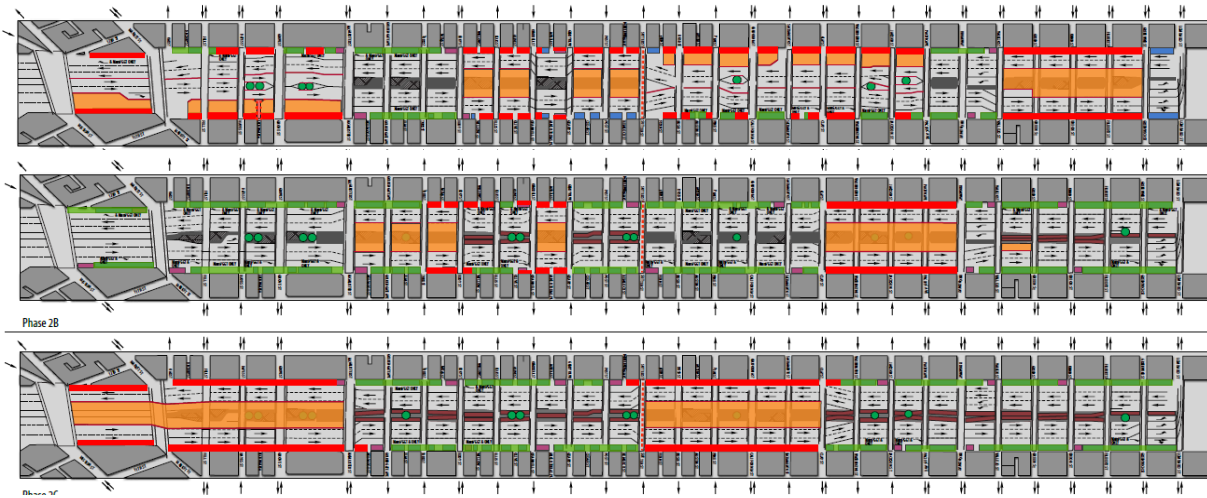

- Phase 3 scheduled fall 2020- fall 2021



	Start	Finish
1A	Fall 2016	Summer 2020*
1B	Summer 2018	Summer 2020*
1C	Summer 2019	Fall 2020*
1D	Fall 2019	Fall 2020*
2	Summer 2020*	Fall 2021*
3	Fall 2020*	Fall 2021*

\*Estimated



# Staff Updates

	Joint Trench %	Sewer %	Water %	Roadway %	Sidewalk %
1A*	100%	100%	100%	100%	85%
1B*	99%	100%	100%	86%	33%
1C*	70%	100%	100%	54%	39%
1D*	88%	100%	100%	6%	7%

- Construction is approximately at 53% completion based on expenditures

# *Staff Updates*

## Construction update

- Wrapping up Utilities Phase
  - Sewer abandonment and punch list remaining
- BRT Buildout Phase has begun
  - Construction in middle of the roadway
  - Construction of red transit-only lanes, median islands, landscaping, bus shelters, bulb-outs, pole setting installations

# Staff Updates

## COVID-19 Resources

- Shared Spaces Program
  - Temporary permits for outside dining and retail
  - Subject to availability
- One-stop resource available for employers and employees at [oewd.org/covid19](https://oewd.org/covid19)
  - Resources
  - Contacts for assistance
  - Updates on new opportunities and programs



## Take your business outside

Free temporary permits for dining and retail.

Find out more:

[www.sf.gov/sharedspaces](https://www.sf.gov/sharedspaces)

SF.GOV

# Staff Updates

- [Additional bus and rail service changes on August 22](#)
- Changes to:
  - L Bus Construction Shuttle
  - 12 Pacific Community Shuttle
  - 28 19<sup>th</sup> Avenue
  - 30 Stockton
  - 44 O'Shaughnessy
  - 49 Van Ness-Mission
  - 54 Felton
- Restored:
  - 7 Haight-Noriega
  - 37 Corbett
  - 45 Union-Stockton
  - 48 Quintara
  - 67 Bernal Heights
- Improved frequency:
  - 8 Bayshore, 9 San Bruno, 9R San Bruno Rapid, 12 Pacific Community Shuttle, 14 Mission, 19 Polk, 22 Fillmore, 24 Divisadero, 25 Treasure Island, 28 19<sup>th</sup> Avenue, 29 Sunset, 43 Masonic, 44 O'Shaughnessy

# Staff Updates

## Geary Rapid Project

As part of the [Geary Rapid Project](#), work to replace aging water and sewer lines between Masonic Street and Van Ness Avenue, in coordination with the San Francisco Public Utilities Commission, continues. Transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, have also started and are being managed by San Francisco Public Works.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact [GearyRapid@SFMTA.com](mailto:GearyRapid@SFMTA.com)

# *Neighboring Project Updates*

## **Lombard Street Vision Zero Project**

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

- General working hours: Monday through Friday, 7:00 a.m. to 3:00 p.m.
- Project completion scheduled June 2020. CalTrans to repave the roadway at a later date.

For more information visit [SFPublicWorks.org/Lombard](https://SFPublicWorks.org/Lombard) or call 415-558-5282



# Staff Updates

- Outreach Updates

- Recent Activities

- Extended deadline for applications to August 15 for Van Ness Business Advisory Committee and Van Ness BRT Community Advisory Committee
    - Van Ness Business Advisory Committee held June 18

- SFPD contract ends 7/31

# *Member Comment*

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

# *Next Meeting*



September 24, 6:00 p.m.

# Thank You



## VAN NESS

IMPROVEMENT  
PROJECT

[SFMTA.com/VanNess](http://SFMTA.com/VanNess)



San Francisco  
Water  
Power  
Sewer

