















### Agenda

#### For those calling in, please mute your phones when not speaking.

- 1. Call to order.
- Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
- 3. Approval of Minutes.
  - a. October 22
- 4. Approval of Chair and Vice-Chair
- 5. SFMTA staff updates.
- Member comment.
- 7. Adjourn.

#### CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.


#### Public Comment

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

# Approval of Minutes


October 22

# Project Schedule

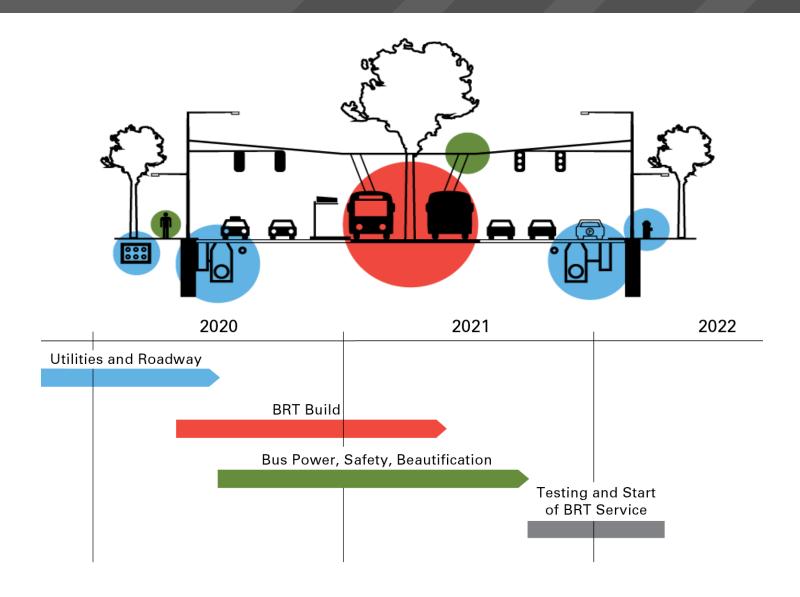


# Project Schedule

Phases 1A and 1B almost complete.



Phases 1C and 1D almost complete.




	Start	Finish		
1A	Fall 2016	Fall 2020*		
1B	Summer 2018	Fall 2020*		
1C	Summer 2019	Fall 2020*		
1D	Fall 2019	Winter 2021*		
2	Summer 2020*	Fall 2021*		
3	Spring 2021*	Winter 2022*		

\*Estimated

# Project Schedule

Phase 2 in progress.

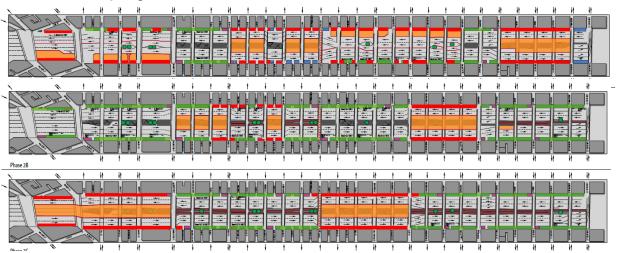

Phase 3 in progress.

\ \ \ \ \ \ \ \	H H	₩ + 1	+ +	+ + +	t + t	H t H	ŧ t ŧt	# # #	# # #
- 12 25 W	3, 3, 4								
					<i>}</i> !!!!!!!			<i>:</i>	
# H	t H	₩ + 1	t Ht t	+ + +	1 + 1	H t H	t t tt	H H H	H H H H
Phase 3A									
<u> </u>	it it	<u> </u>	† <del>†</del> † †	+ + +	<u> </u>	<del></del>	+ + +	11 11 11	it it it it
					estables to the state of the st				
				-11-11-11				네는중네요	

	Start	Finish
1A	Fall 2016	Fall 2020*
1B	Summer 2018	Fall 2020*
1C	Summer 2019	Fall 2020*
1D	Fall 2019	Winter 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Winter 2022*

\*Estimated

	Joint Trench %	Sewer %	Water %	Roadway %	Sidewalk %
1A*	100%	100%	100%	100%	87%
1B*	100%	100%	100%	86%	33%
1C*	100%	100%	100%	82%	73%
1D*	100%	100%	100%	44%	36%

• Construction is approximately at 58.95% completion based on expenditures

### Construction update

- BRT Buildout Phase has begun
  - Construction in middle of the roadway
  - Construction of red transit-only lanes, median islands, landscaping, bus shelters, bulb-outs, pole setting installations



### Contract Modification 12

 Compensates contractor for costs related to pedestrian monitoring services in the amount of \$2,589,381, for a total Contract amount not to exceed \$220,507,216, with no time extension.

- Directed Business Support Program closed
  - Funding of \$5,000-\$10,000 available to eligible businesses; currently finalizing eligibility and awarding funds
- SF Shines Storefront Improvement Program
  - Grants and design services for businesses to improve their storefronts, including COVID-19 safety measures
  - Administered by OEWD, details at <u>sf.gov/sf-shines</u>

#### **Geary Rapid Project**

As part of the Geary Rapid Project, work to replace aging water and sewer lines between Masonic Street and Van Ness Avenue, in coordination with the San Francisco Public Utilities Commission, continues. Transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, have also started and are being managed by San Francisco Public Works.

For more information visit SFMTA.com/Geary or contact GearyRapid@SFMTA.com

# Neighboring Project Updates

#### **Lombard Street Vision Zero Project**

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

- General working hours: Monday through Friday, 7:00 a.m. to 3:00 p.m.
- Project completion scheduled June 2020. CalTrans to repave the roadway at a later date.

For more information visit SFPublicWorks.org/Lombard or call 415-558-5282

- Outreach Updates
  - Recent Activities
    - Canvassing for Directed Business Support program
    - Quarterly summer newsletter sent by email
  - Upcoming outreach activities
    - Quarterly fall newsletter to be sent by mail

### Member Comment

 Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

# Next Meeting



January 28, 6:00 p.m.

### Thank You



VAN NESS

IMPROVEMENT PROJECT

SFMTA.com/VanNess













