

VAN NESS

IMPROVEMENT PROJECT



Van Ness BRT CAC

January 28



Agenda

For those calling in, please mute your phones when not speaking.

1. Call to order.
2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
3. Approval of Minutes.
 - a. November 19, 2020
4. SFMTA staff updates.
5. Member comment.
6. Adjourn.

CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.


Public Comment

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes


- November 19, 2021

Project Schedule

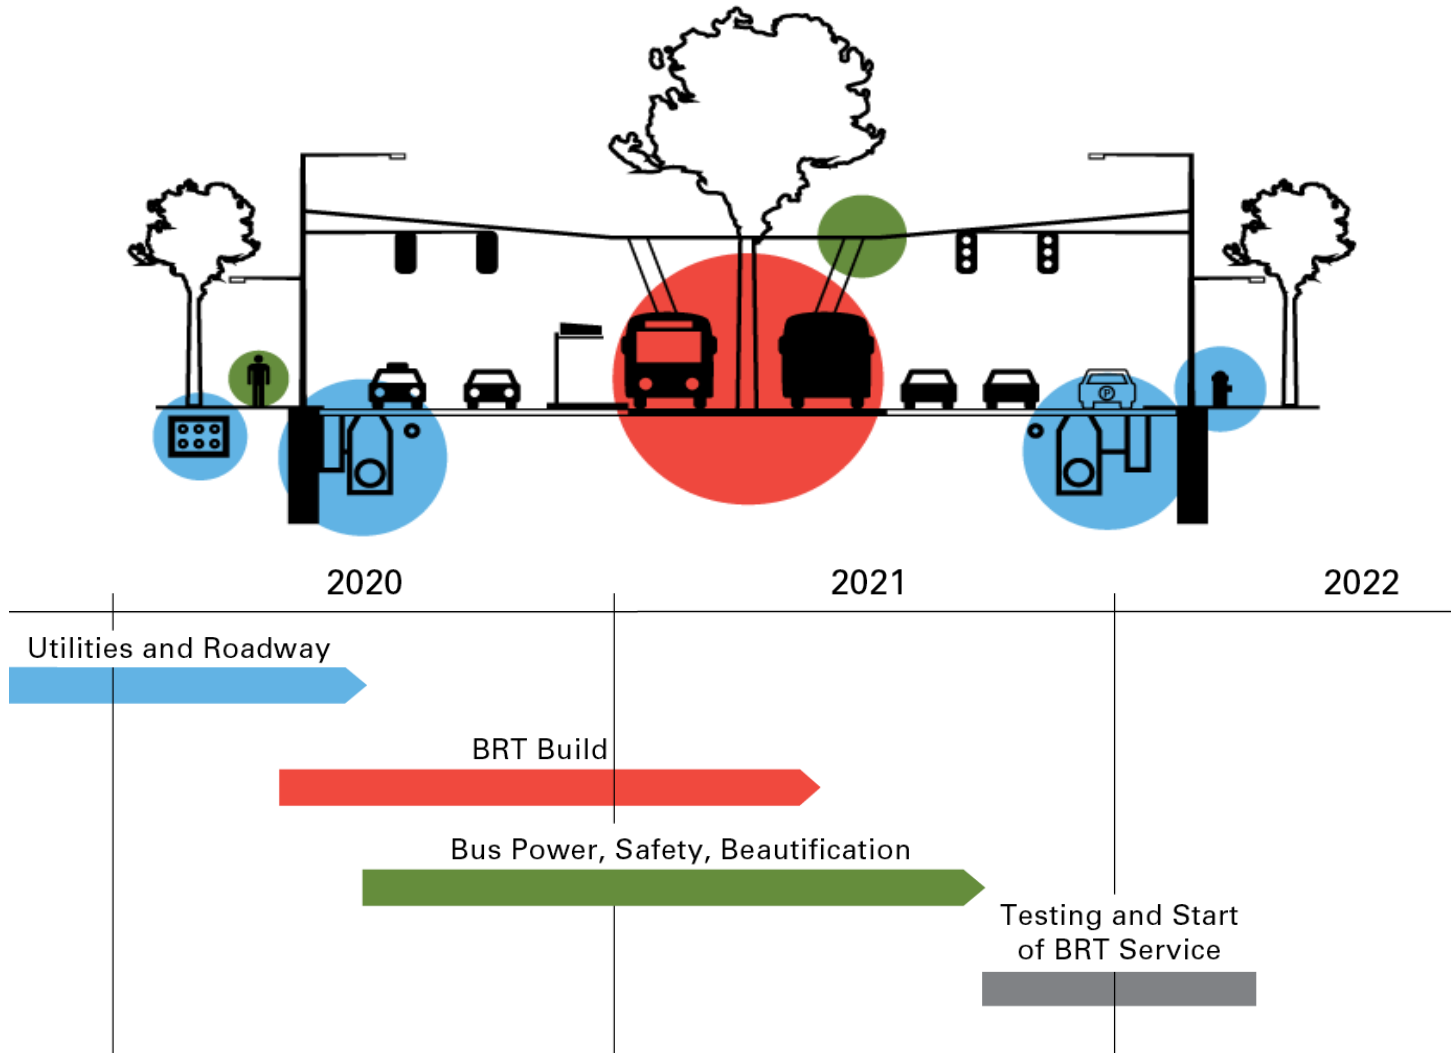


Project Schedule

- Phases 1A and 1B almost complete.




Phase 1A



Phase 1B

- Phases 1C and 1D almost complete.



Phase 1C




Phase 1D

	Start	Finish
1A	Fall 2016	Winter 2021*
1B	Summer 2018	Spring 2021*
1C	Summer 2019	Winter 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020	Fall 2021*
3	Spring 2021*	Fall 2021*

*Estimated

Project Schedule

- Phase 2 underway. Expected completion fall 2021.

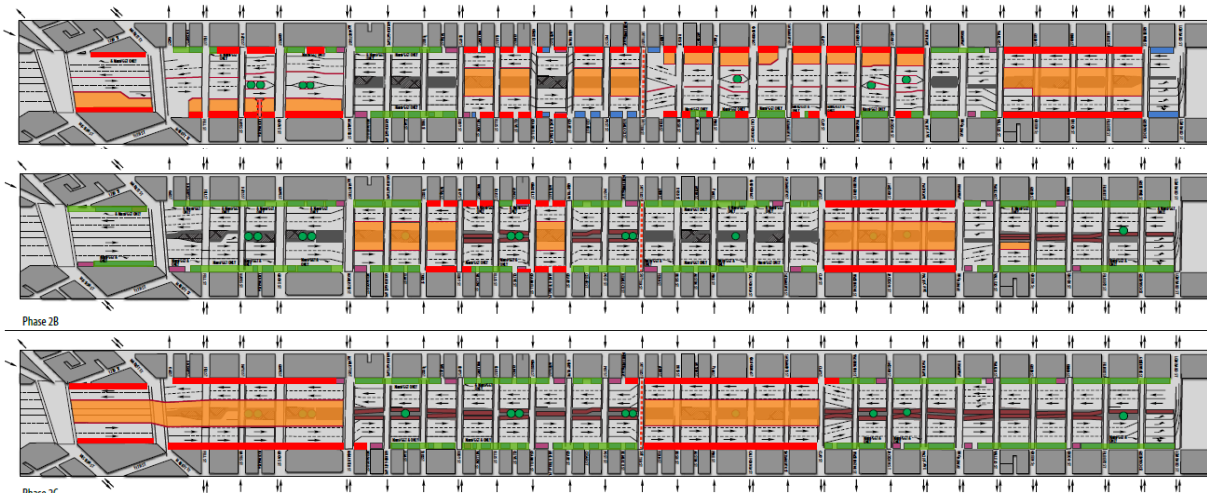

- Phase 3 underway. Expected completion fall 2021.



	Start	Finish
1A	Fall 2016	Winter 2021*
1B	Summer 2018	Spring 2021*
1C	Summer 2019	Winter 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020	Fall 2021*
3	Spring 2021*	Fall 2021*

*Estimated

Staff Updates

	Utilities %	Roadway %	Sidewalk %
1A*	100%	100%	87%
1B*	100%	86%	49%
1C*	100%	82%	73%
1D*	100%	46%	38%

- Construction is approximately at 62.96% completion based on expenditures

Staff Updates

Construction update

- BRT Buildout Phase in progress
 - Construction of median islands, bus shelters, bulb-outs
 - Installation of red transit lanes, pole setting



Staff Updates

- Directed Business Support Program re-opened
 - Funding of \$5,000-10,000 available to eligible businesses; deadline now January 31, 2021.
- Corridor marketing plan being presented to Business Advisory Committee

Staff Updates

Geary Rapid Project

As part of the [Geary Rapid Project](#), work to replace aging water lines, in coordination with San Francisco Public Utilities Commission, continues. Surface transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, are also underway and are being managed by San Francisco Public Works.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Neighboring Project Updates

Lombard Street Vision Zero Project


The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

- General working hours: Monday through Friday, 7:00 a.m. to 3:00 p.m.
- Project completion scheduled June 2020. Caltrans to repave the roadway at a later date.

For more information visit SFPublicWorks.org/Lombard or call 415-558-5282

Staff Updates

- Outreach Updates
 - Upcoming outreach activities
 - Quarterly winter newsletter to be sent by email

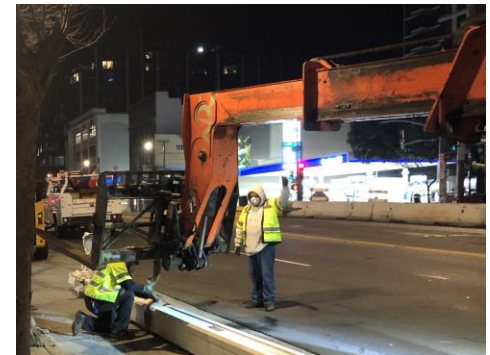

Member Comment

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

Next Meeting



March 25, 6:00 p.m.

Thank You



VAN NESS



SFMTA.com/VanNess



San Francisco
Water
Power
Sewer

