

VAN NESS

IMPROVEMENT PROJECT



Van Ness BRT CAC

March 25



Agenda

For those calling in, please mute your phones when not speaking.

1. Call to order.
2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
3. Approval of Minutes.
 - a. [February 25, 2021](#)
4. SFMTA staff updates.
5. Member comment.
6. Adjourn.

CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.


Public Comment

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes



- February 25, 2021

Project Schedule


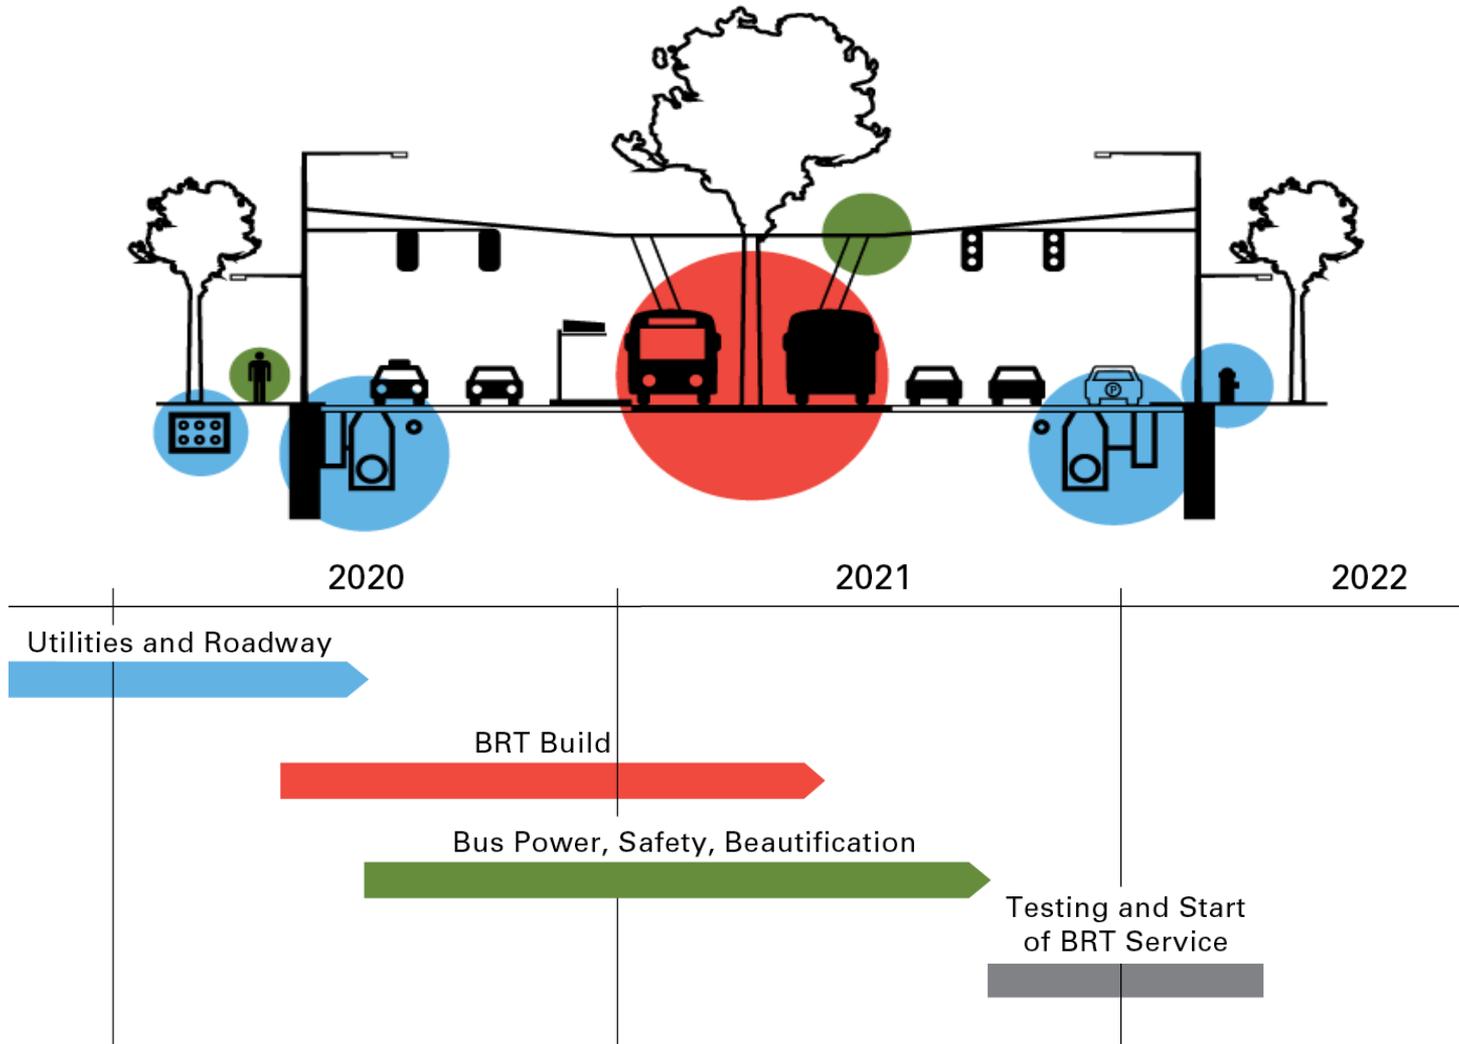


Project Schedule

- Phases 1A and 1B almost complete.



- Phases 1C and 1D almost complete.




	Start	Finish
1A	Fall 2016	Spring 2021*
1B	Summer 2018	Winter 2021*
1C	Summer 2019	Spring 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020	Spring 2021*
3	Spring 2021*	Fall 2021*

*Estimated

Project Schedule

- Phase 2 underway. Expected completion fall 2021.

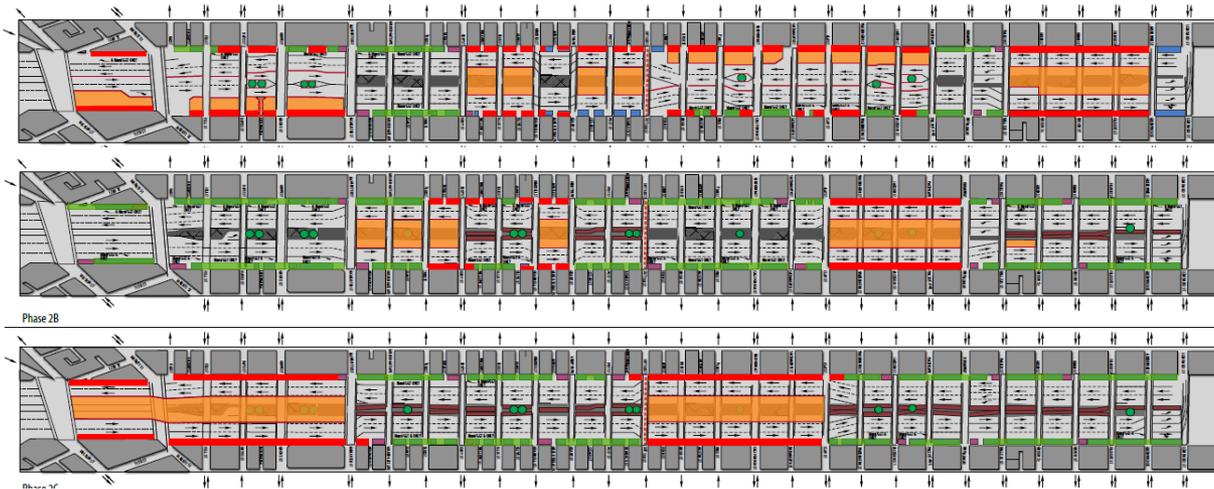

- Phase 3 underway. Expected completion fall 2021.



	Start	Finish
1A	Fall 2016	Spring 2021*
1B	Summer 2018	Winter 2021*
1C	Summer 2019	Spring 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020	Spring 2021*
3	Spring 2021*	Fall 2021*

*Estimated

Staff Updates

	Utilities%	Roadway %	Sidewalk %
1A*	100%	100%	89%
1B*	100%	86%	66%
1C*	100%	82%	86%
1D*	100%	54%	40%

- Construction is approximately at 67.16% completion based on expenditures

Staff Updates

Construction update

- BRT Buildout Phase in progress
 - Construction of median islands, bus shelters, bulb-outs
 - Installation of red transit lanes, pole setting, overhead contact system wiring
 - Paving



Staff Updates

- Corridor marketing plan being presented to Business Advisory Committee

Staff Updates

Geary Rapid Project

As part of the [Geary Rapid Project](#), work to replace aging water lines, in coordination with San Francisco Public Utilities Commission, continues. Surface transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, are also underway and are being managed by San Francisco Public Works.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Neighboring Project Updates


Caltrans Lombard Street Daytime Lane Closures

Follows the Lombard Vision Zero Project and includes repaving the roadway, restriping the lanes and crosswalk and upgrading curb ramps for ADA. On US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue. Construction is planned March through July, Monday through Friday, 7:00 a.m. to 6:00 p.m.

For real-time information, please visit Caltrans QuickMap: quickmap.dot.ca.gov

Staff Updates

- Outreach Updates
 - Recent outreach activities
 - FTA Quarterly Update
 - Upcoming outreach activities
 - Spring newsletter to be sent by mail
 - Distribution of branded PPE to Van Ness corridor businesses

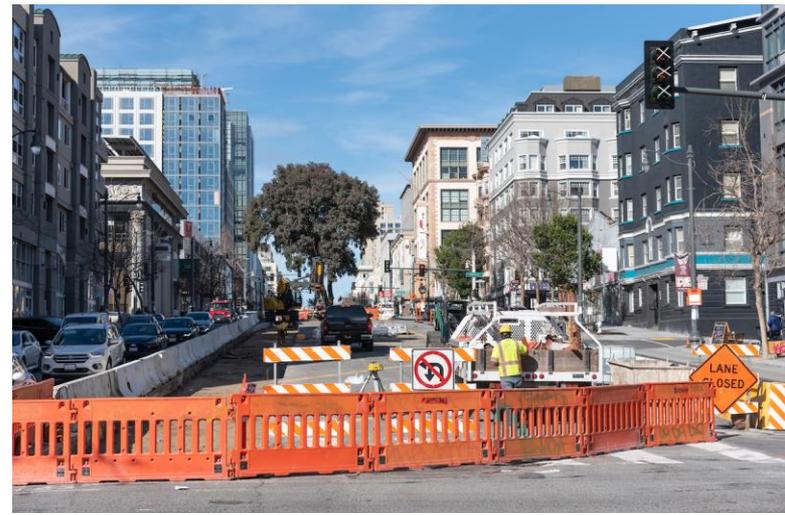

Member Comment

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

Next Meeting



May 27, 6:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess



San Francisco
Water
Power
Sewer

