

VAN NESS

IMPROVEMENT PROJECT



Van Ness BRT CAC

March 28



Agenda

1. Call to order. Van Ness BRT Community Advisory Committee members please sit at table.
2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
3. Approval of Minutes – February 28.
4. Presentation, discussion and possible action regarding letter of support for proposed public art on project corridor.
5. SFMTA staff updates.
6. Member comment.
7. Adjourn.

CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum
- If no quorum can be reached, meeting to be canceled

Public Comment




- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes

- February 28.



Letter of Support for Public Art

- [Draft](#) available for discussion
 - Emailed to committee members Monday, March 25, 1:56 p.m.
 - Subject: Van Ness BRT CAC Letter of Support for Public Art- DRAFT
- Motion required to edit/approve
 - Motion
 - Second
 - Discussion
 - Vote

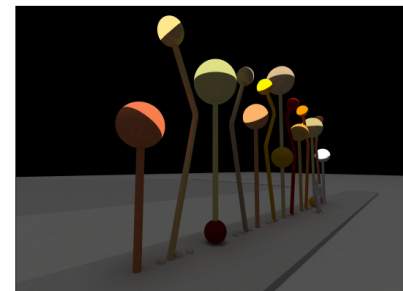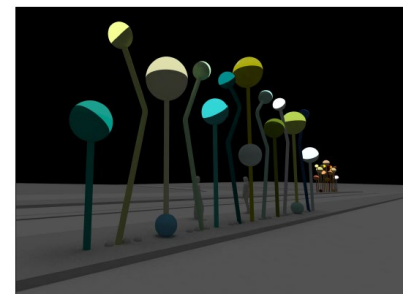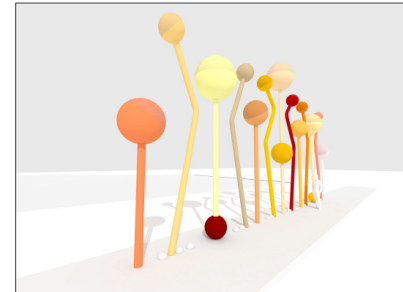



Staff Updates

- Project schedule

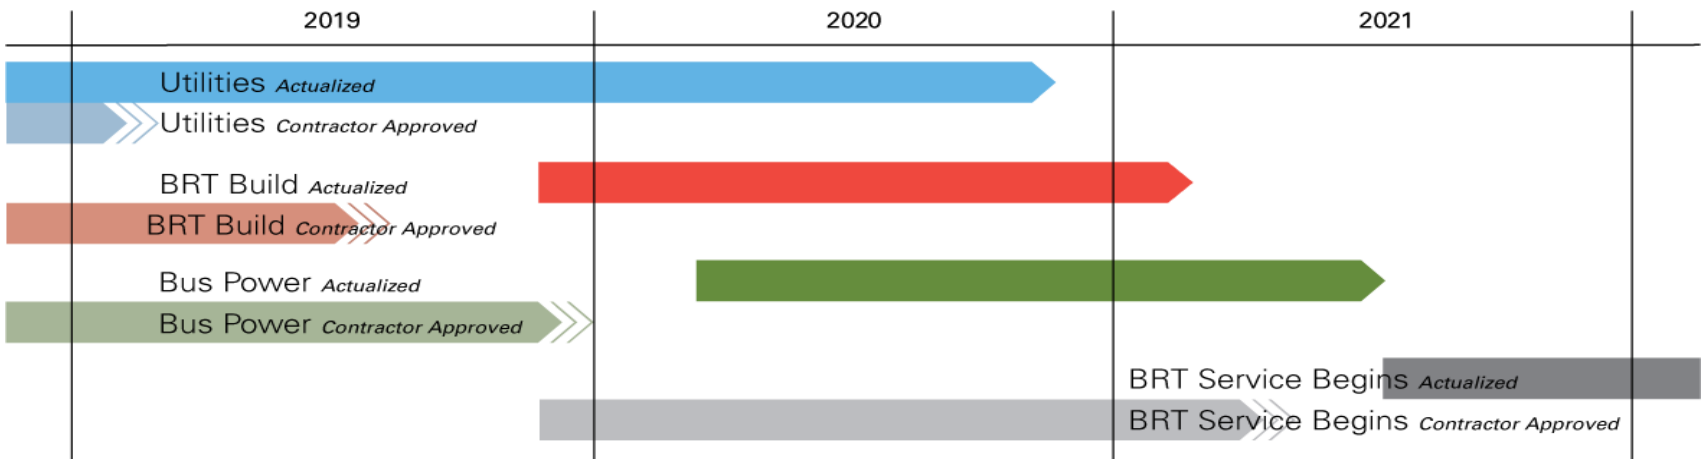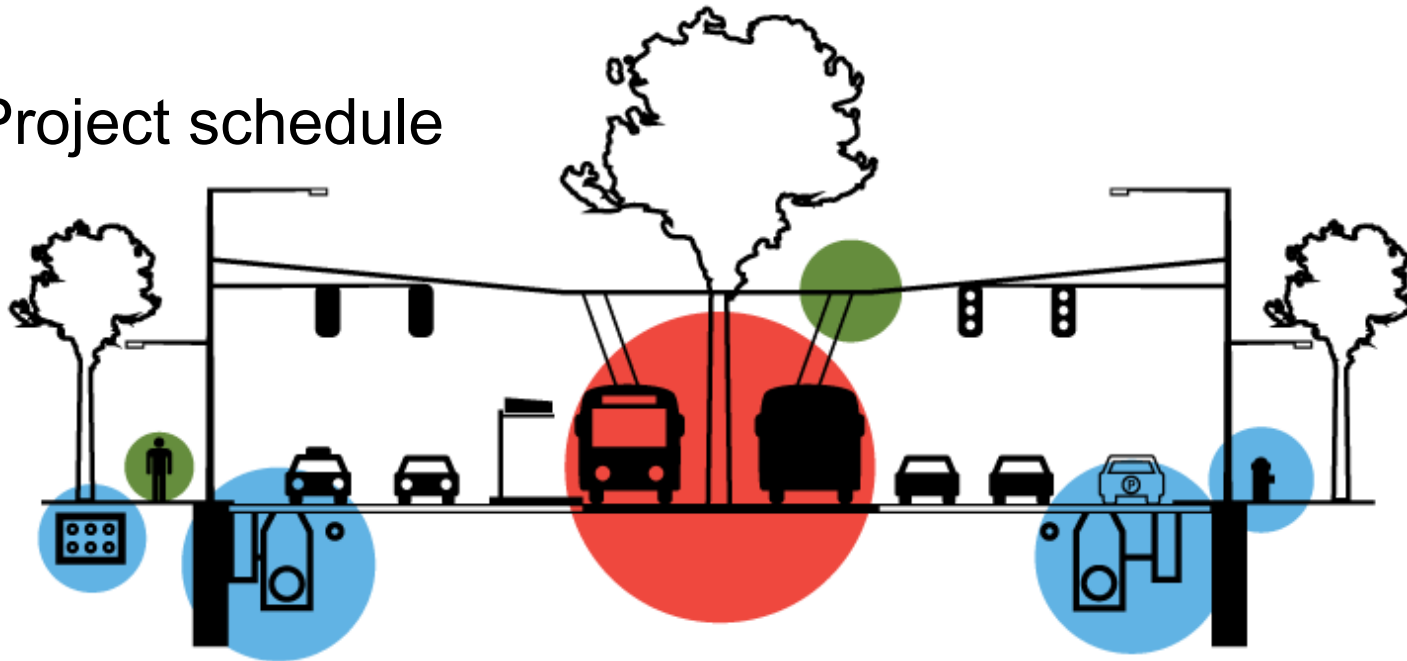

Staff Updates



- Phases 1A and 1B underway. Expected completion summer 2019



	Start	Finish
1A	Fall 2016	Spring 2019*
1B	Summer 2018	Summer 2019*
1C	Summer 2019*	Summer 2020*
1D	Summer 2019*	Spring 2020*
2	Winter 2020*	Winter 2021*
3	Spring 2020*	Spring 2021*


*Estimated

- Phases 1C and 1D scheduled summer 2019-spring 2020



Staff Updates


- Phase 2 scheduled winter 2020-winter 2021

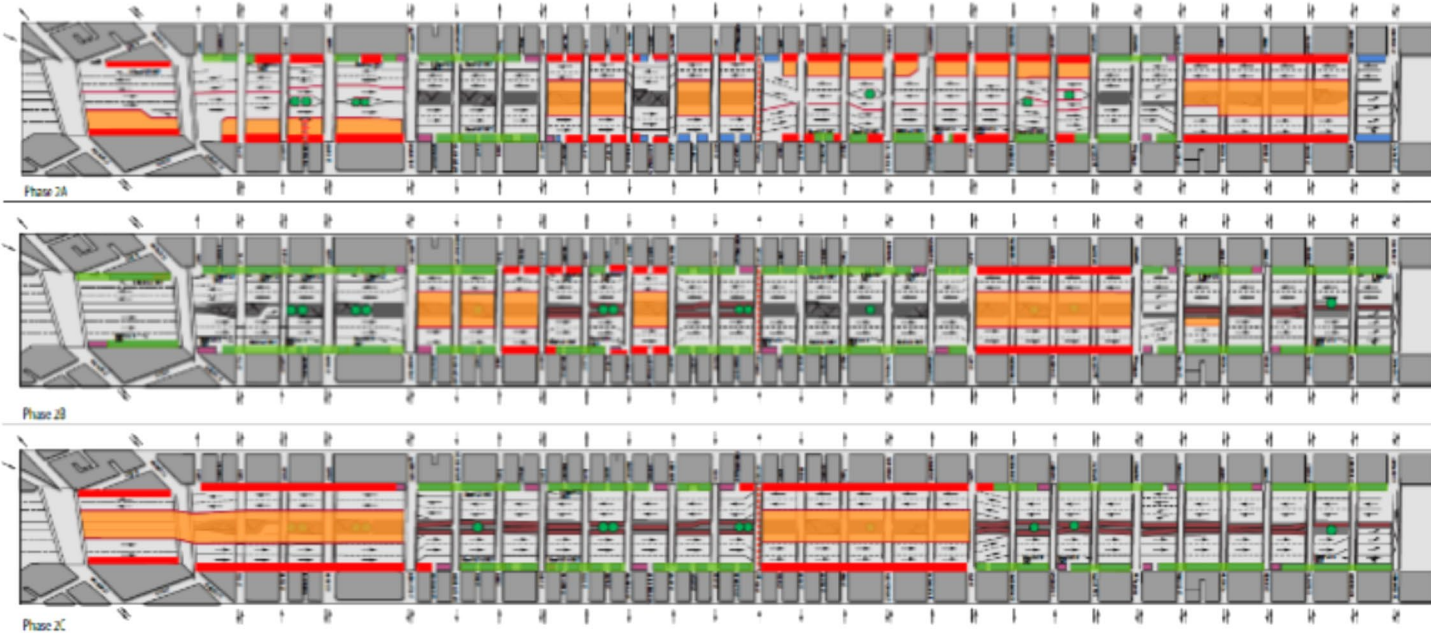

	Start	Finish
1A	Fall 2016	Spring 2019*
1B	Summer 2018	Summer 2019*
1C	Summer 2019*	Summer 2020*
1D	Summer 2019*	Spring 2020*
2	Winter 2020*	Winter 2021*
3	Spring 2020*	Spring 2021*

*Estimated

- Phase 3 scheduled spring 2020-spring 2021

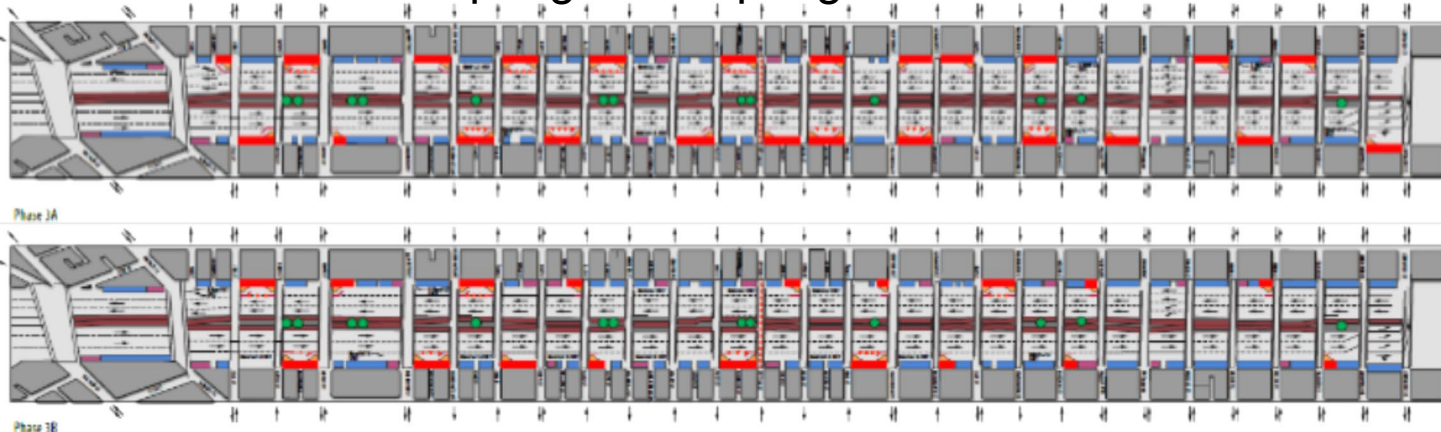

Staff Updates

Construction update


- Construction is approximately at 28% completion (27% in January)
- Joint trenching ongoing
- Addressing utility conflicts
- Sewer installation – intensive night work
- Sidewalk replacement work – outreach to affected blocks ongoing
- SFPD additional nighttime foot patrols and increased enforcement of construction zones



Staff Updates


- Accelerating work where possible
 - Procedural adjustments
 - Special Traffic Permits to extend workhours
 - Seeking Caltrans permission for weekend daytime traffic lane shut downs
 - Advance identification of major conflicts
 - Updates of project design
 - Exploratory potholing
 - Mapping subsurface conflicts
 - Changing chlorination activity from 5 working to 7 calendar days
 - Water resequencing
 - Slip lining to reduce days of sewer work
 - Trolley wire installation after OCS pole installation
 - OCS duct bank installation independent of utility work
 - Increasing staff capacity
 - 6-day work weeks
 - Strategic use of double shifts
 - Allocating more staff resources to project delivery

Staff Updates

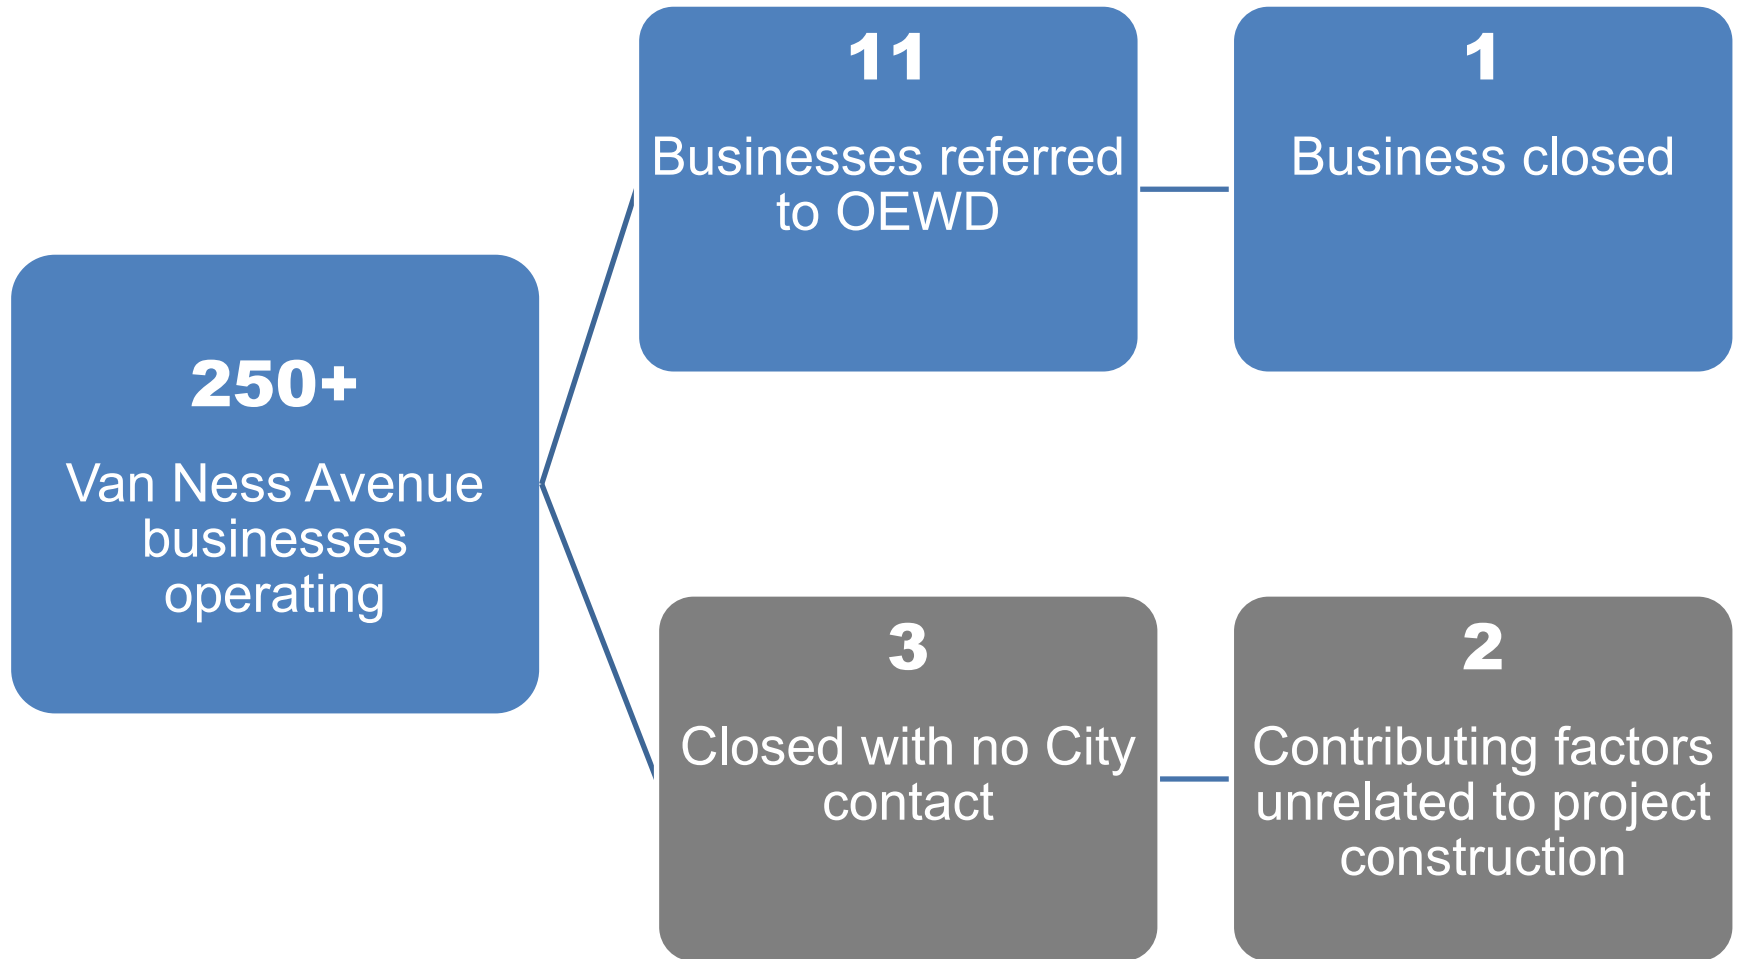

Staff Updates

- Outreach Updates

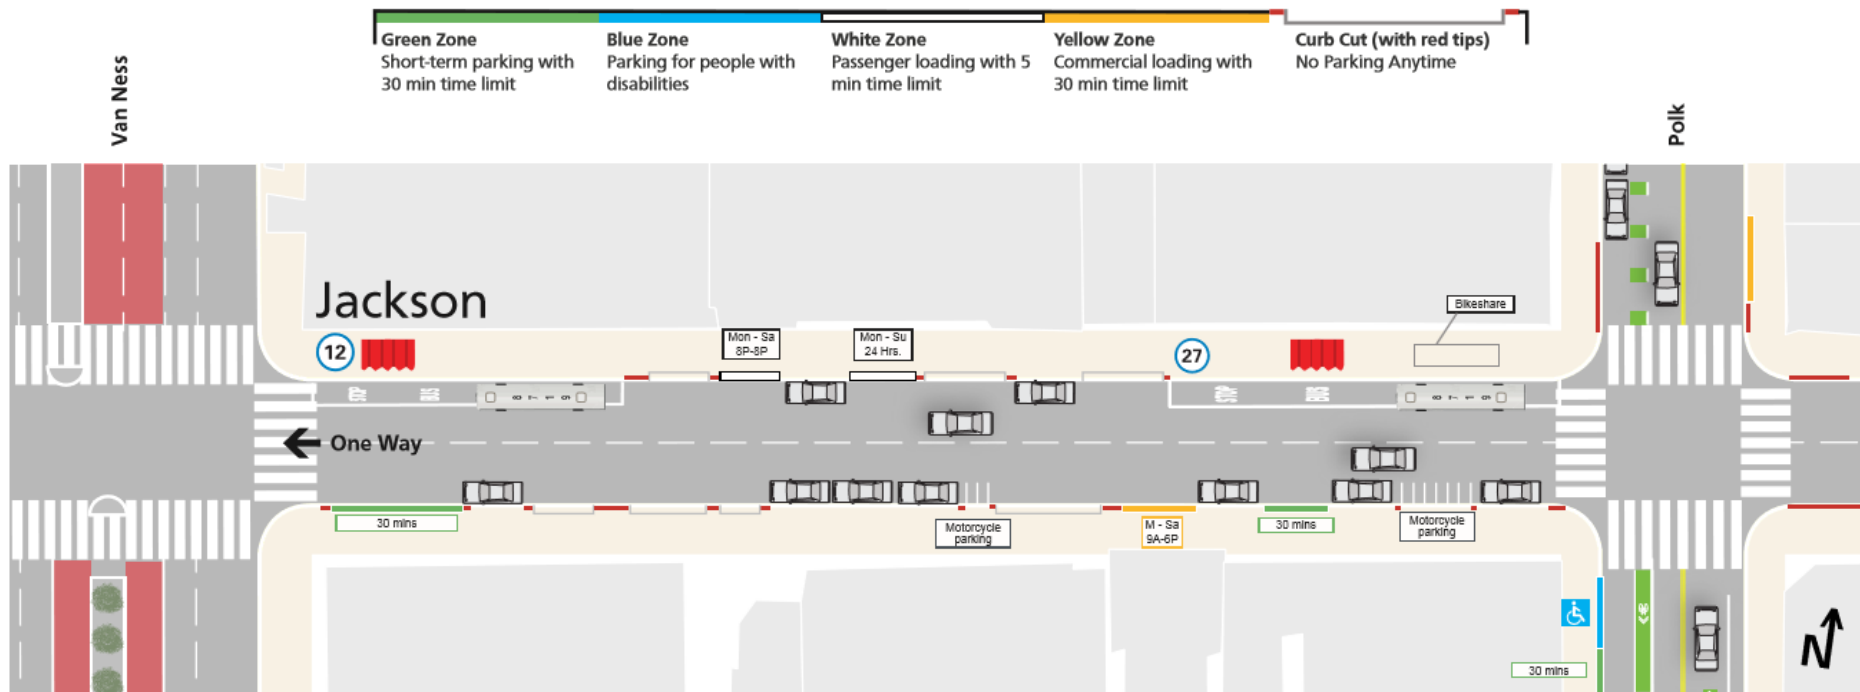

12 Folsom & 27 Bryant Terminals
Proposal for Safer Transit Operations and Parking & Loading Zone Changes

Spring 2019

Staff Updates

- **Outreach Updates**

- **Recent Milestones**

- Meet the Expert at Alborz Restaurant, March 6
 - Digital Newsletter distributed March 18
 - Transportation Authority Board of Commissioners, March 19
 - Van Ness Business Advisory Committee, March 21
 - SFCTA Citizens Advisory Committee Meeting, March 27

Staff Updates

- Outreach Updates

- Upcoming outreach activities

- Meet the Expert: April 4, 6:00 p.m.
 - Geary Rapid
 - Tommy's Joynt, 1101 Geary Blvd (at Van Ness)
 - Van Ness Business Advisory Committee
 - April 18, 3:00 p.m.
 - 1 South Van Ness Avenue
 - Civic Center Conference Room, 3rd Floor
 - SFCTA Board of Commissioners
 - April 23, 10:00 a.m.
 - City Hall, Room 250
 - SFCTA Citizens Advisory Committee
 - April 24, 6:00 p.m.
 - SFCTA, 1455 Market Street, 22nd Floor

Staff Updates

Polk Streetscape Project

Most construction work for the project has been completed. Crews are wrapping up work and performing final striping changes.

Ribbon cutting and community celebration

Tuesday, April 2, 11:00 a.m.-12:00 p.m.

Entrance at Fern Alley at Polk Street

Find out more at sfpublicworks.org/polk.

Find out more and sign up for project updates at sfpublicworks.org/polk.



Staff Updates

Geary Rapid Project

The first phase of construction as part of the Geary Rapid Project has begun. Work to replace aging water and sewer lines between Masonic and Van Ness avenues is scheduled to be done in coordination with the San Francisco Public Utilities Commission (SFPUC).

Water main replacement work scheduled on eastbound Geary Boulevard between St. Joseph's Avenue and Scott Street. Parking will be temporarily restricted on the south side of Geary Boulevard until work is complete. Inbound bust stop on Geary at Divisadero will be relocated slightly west during water work.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Staff Updates

Lombard Street Vision Zero Project

- Pedestrian safety, transit performance, and utility improvements (Lombard Street at Richardson)
- Final paving to be done along Lombard Street
- Crews are scheduled to continue installing new water main working west from Fillmore Street to Richardson Avenue. This work will be performed primarily on the north side of Lombard Street with occasional work that crosses the south side of Lombard at some intersections. This work is expected to continue through April 2019.
- General working hours Monday through Friday 7:00 a.m. to 3:00 p.m.
- For more information visit SFPublicWorks.org/Lombard or Call 415-558-5282

Member Comment

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

Next Meeting



May 23, 6:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

sfmta.com/vanness

