

# VAN NESS

# IMPROVEMENT PROJECT



*Van Ness BAC*  
*February 18, 2021*



# *Agenda*

1. Call to order.
2. Public comment for matters within BAC jurisdiction not on today's calendar.
3. Approval of Minutes – not applicable.
4. SFMTA staff updates.
5. Member comment.
6. Corridor marketing efforts.
7. Adjourn.

# *BAC administration reminder*

- BAC members are asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

# *Public Comment*


- See Public Comment Policy on back of agenda.
- Public comment for matters that are within the Van Ness Business Advisory Committee jurisdiction and are not on today's calendar.

# *Approval of Minutes*

**None.**



# Staff updates

- Project update


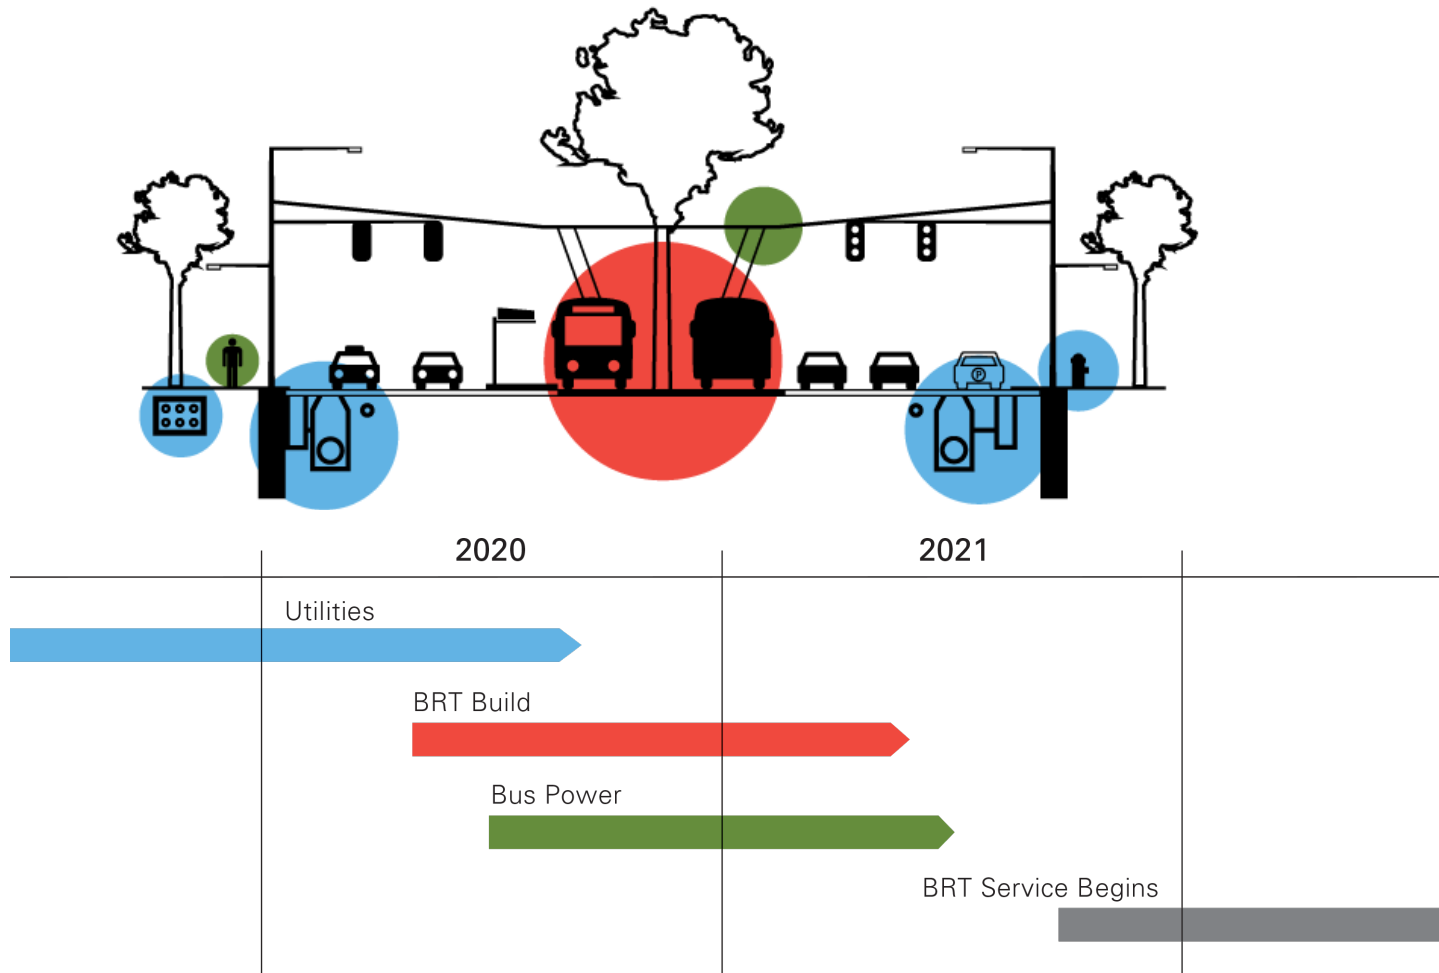


# Project Schedule

- Phases 1A and 1B almost complete.



- Phases 1C and 1D almost complete.




	Start	Finish
1A	Fall 2016	Winter 2021*
1B	Summer 2018	Summer 2021*
1C	Summer 2019	Summer 2021*
1D	Fall 2019	Fall 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Fall 2021*

\*Estimated

# Project Schedule

- Phase 2 in progress.

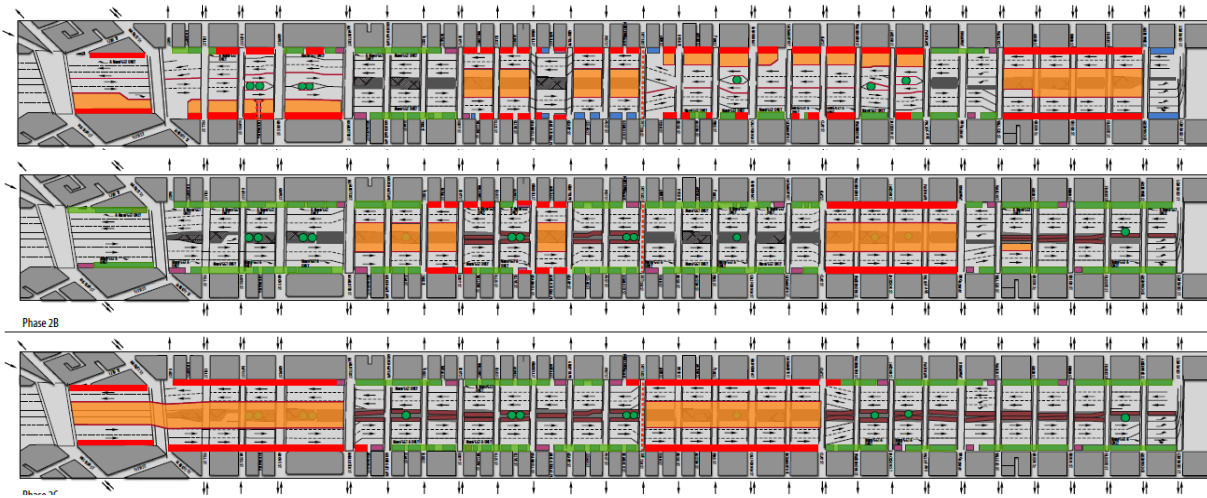

- Phase 3 in progress.



	Start	Finish
1A	Fall 2016	Winter 2021*
1B	Summer 2018	Summer 2021*
1C	Summer 2019	Summer 2021*
1D	Fall 2019	Fall 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Fall 2021*

\*Estimated



# Staff Updates

## Construction update

- BRT Buildout Phase in progress
  - Construction of red transit-only lanes, median islands, landscaping, bus shelters, bulb-outs, pole setting installations



# Staff Updates

## Outreach Updates

### – Recent Activities

- Quarterly spring newsletter sent by email
- Applications closed for Directed Business Support Program

### – Upcoming outreach activities

- Quarterly spring newsletter to be sent by mail



# Staff Updates

## Geary Rapid Project

As part of the [Geary Rapid Project](#), work to replace aging water lines, in coordination with San Francisco Public Utilities Commission, continues. Surface transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, are also underway and are being managed by San Francisco Public Works.

For more information visit [SFMTA.com/Geary](https://SFMTA.com/Geary) or contact [GearyRapid@SFMTA.com](mailto:GearyRapid@SFMTA.com)

# *Neighboring Project Updates*

## **Lombard Street Vision Zero Project**

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

- General working hours: Monday through Friday, 7:00 a.m. to 3:00 p.m.
- Project completed, with Caltrans to repave the roadway soon.

For more information visit [SFPublicWorks.org/Lombard](http://SFPublicWorks.org/Lombard) or call 415-558-5282

# *Next Meeting*



June 17, 1:00 p.m.

# Thank You



## VAN NESS

IMPROVEMENT  
PROJECT

[SFMTA.com/VanNess](http://SFMTA.com/VanNess)

