

# VAN NESS

# IMPROVEMENT PROJECT



## *Van Ness BRT CAC* *June 25*



# Agenda

***For those calling in, please mute your phones when not speaking.***

1. Call to order.
2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
3. Approval of Minutes.
  - a. April 23 and May 28
4. SFMTA staff updates.
5. Member comment.
6. Adjourn.

# *CAC administration reminder*

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.



# *Public Comment*

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

# *Approval of Minutes*


- April 23.
- May 28.

# Project Schedule

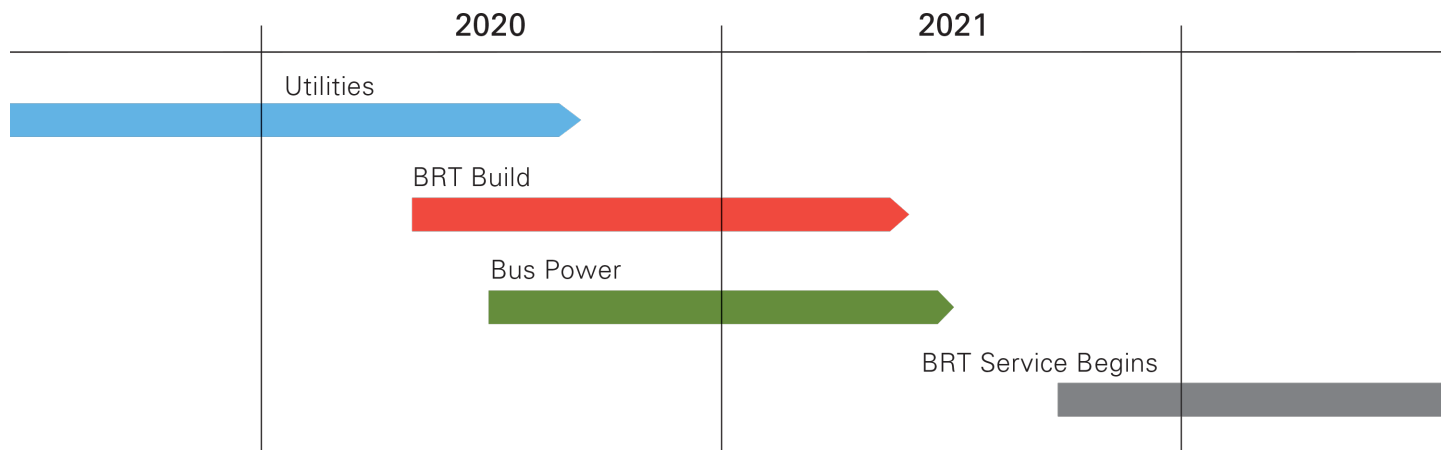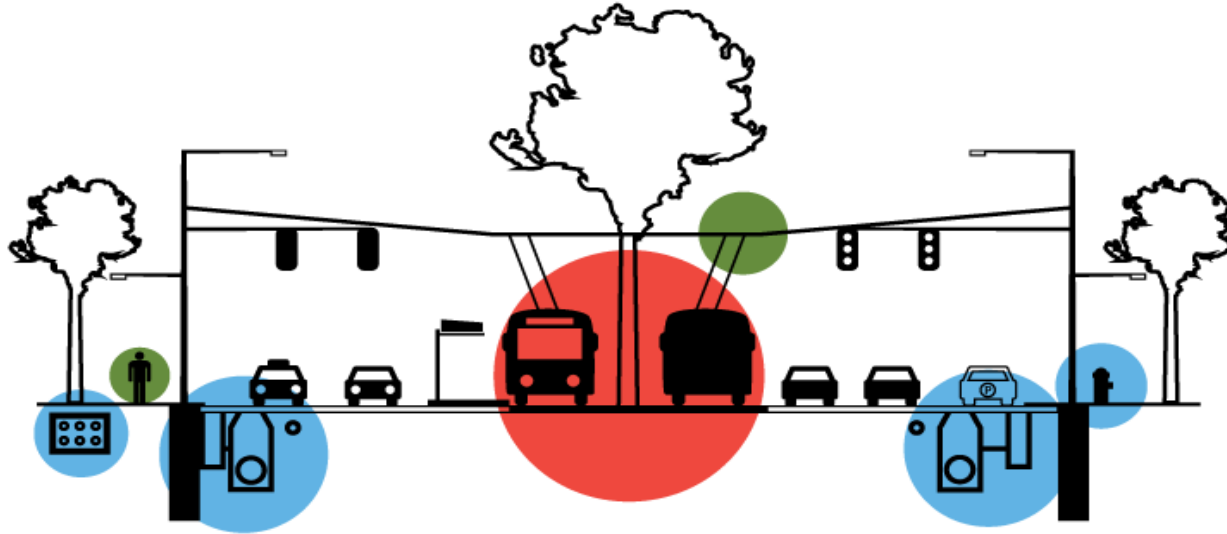


# Project Schedule

- Phases 1A and 1B underway. Expected completion summer 2020




Phase 1A




Phase 1B

- Phases 1C and 1D underway. Expected completion summer 2020



Phase 1C



Phase 1D


	Start	Finish
1A	Fall 2016	Summer 2020*
1B	Summer 2018	Summer 2020*
1C	Summer 2019	Summer 2020*
1D	Fall 2019	Fall 2020*
2	Spring 2020*	Summer 2021*
3	Fall 2020*	Summer 2021*

\*Estimated



# Project Schedule

- Phase 2 scheduled spring 2020-summer 2021

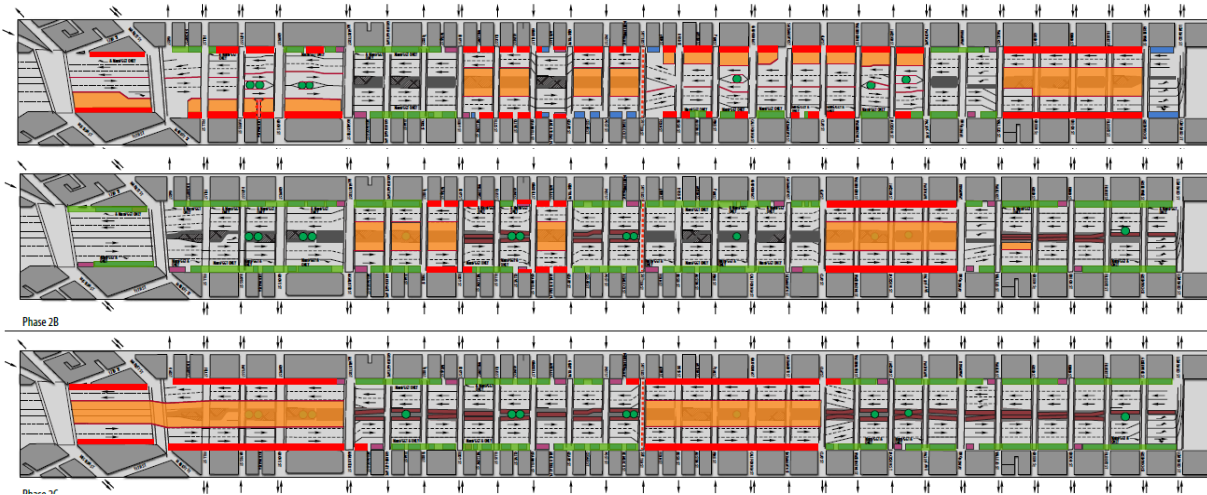

- Phase 3 scheduled fall 2020-summer 2021



	Start	Finish
1A	Fall 2016	Summer 2020*
1B	Summer 2018	Summer 2020*
1C	Summer 2019	Summer 2020*
1D	Fall 2019	Fall 2020*
2	Spring 2020*	Summer 2021*
3	Fall 2020*	Summer 2021*

\*Estimated



# Staff Updates

	Joint Trench %	Sewer %	Water %	Roadway %	Sidewalk %
1A*	100%	100%	100%	100%	82%
1B*	99%	99%	99%	86%	33%
1C*	70%	99%	99%	35%	19%
1D*	88%	95%	95%	6%	5%
<b>Total*%</b>	<b>82%</b>	<b>74%</b>	<b>93%</b>	<b>54%</b>	<b>53%</b>

\*Total % complete is the most accurate estimate of the overall progress of the project.

- Construction is approximately at 51.84% completion based on expenditures

# *Staff Updates*

## Construction update

- Wrapping up Utilities Phase
  - Joint trenching, utility conflicts, sidewalk replacement, street base repair and paving work, sewer and water installation
- Shifting to BRT Buildout Phase this summer
  - Construction in middle of the roadway
  - Construction of red transit-only lanes, median islands, landscaping, bus shelters, bulb-outs, pole setting installations

# Staff Updates

## COVID-19 Resources

- Shared Spaces Program
  - Temporary permits for outside dining and retail
  - Subject to availability
- One-stop resource available for employers and employees at [oewd.org/covid19](https://oewd.org/covid19)
  - Resources
  - Contacts for assistance
  - Updates on new opportunities and programs



## Take your business outside

Free temporary permits for dining and retail.

Find out more:

[www.sf.gov/sharedspaces](https://www.sf.gov/sharedspaces)

SF.GOV



# Staff Updates

## Geary Rapid Project

As part of the [Geary Rapid Project](#), work to replace aging water and sewer lines between Masonic Street and Van Ness Avenue, in coordination with the San Francisco Public Utilities Commission, continues. Transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, have also started and are being managed by San Francisco Public Works.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact [GearyRapid@SFMTA.com](mailto:GearyRapid@SFMTA.com)



# *Neighboring Project Updates*

## **Lombard Street Vision Zero Project**

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

- General working hours: Monday through Friday, 7:00 a.m. to 3:00 p.m.
- Project completion scheduled June 2020. CalTrans to repave the roadway at a later date.

For more information visit [SFPublicWorks.org/Lombard](https://SFPublicWorks.org/Lombard) or call 415-558-5282



# *Staff Updates*

- **Outreach Updates**

- **Recent Activities**

- Recruiting for Van Ness Business Advisory Committee and Van Ness BRT Community Advisory Committee– Applications due June 30
    - Van Ness Business Advisory Committee held June 18

# *Member Comment*

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

# *Next Meeting*



August 27, 6:00 p.m.

# Thank You



## VAN NESS

IMPROVEMENT  
PROJECT

[SFMTA.com/VanNess](http://SFMTA.com/VanNess)

