

VAN NESS

IMPROVEMENT PROJECT



Van Ness BRT CAC

June 24, 2021



Agenda

For those calling in, please mute your phones when not speaking.

1. Call to Order.
2. Public comment: Members of the public may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar
3. Approval of minutes – April 22, 2021.
4. Presentation, discussion and possible action regarding update from SFMTA staff.
 - Project Schedule.
 - Construction update.
 - Update on neighboring projects.
 - Business support update.
 - Outreach update.
5. Member comment: Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar
6. Adjourn

CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

Public Comment


- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes


- April 22, 2021

Project Schedule

- Phases 1A and 1B almost complete.

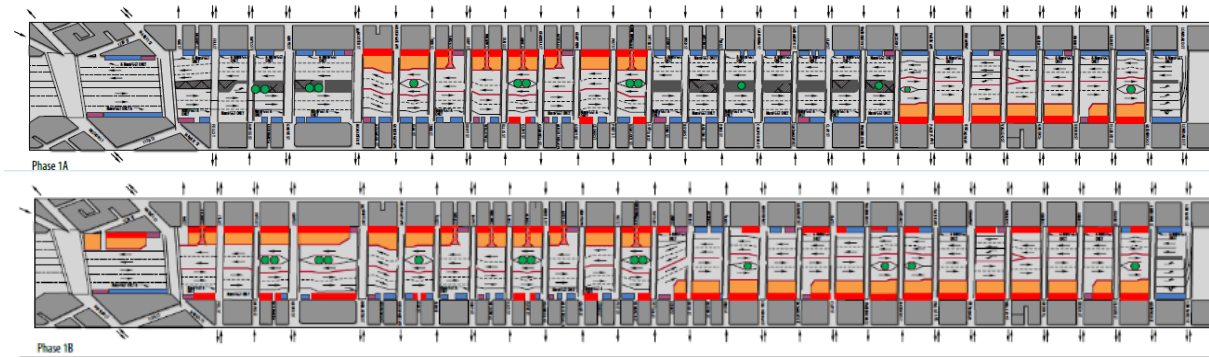

- Phases 1C and 1D almost complete.

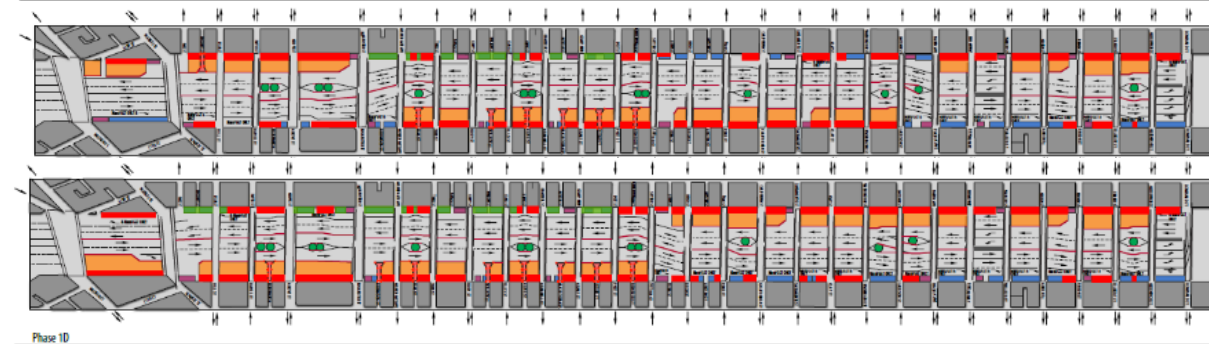


	Start	Finish
1A	Fall 2016	Winter 2022*
1B	Summer 2018	Summer 2021*
1C	Summer 2019	Winter 2022*
1D	Fall 2019	Summer 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Summer 2021 to Fall 2021*

*Estimated

Project Schedule

- Phase 2 in progress.

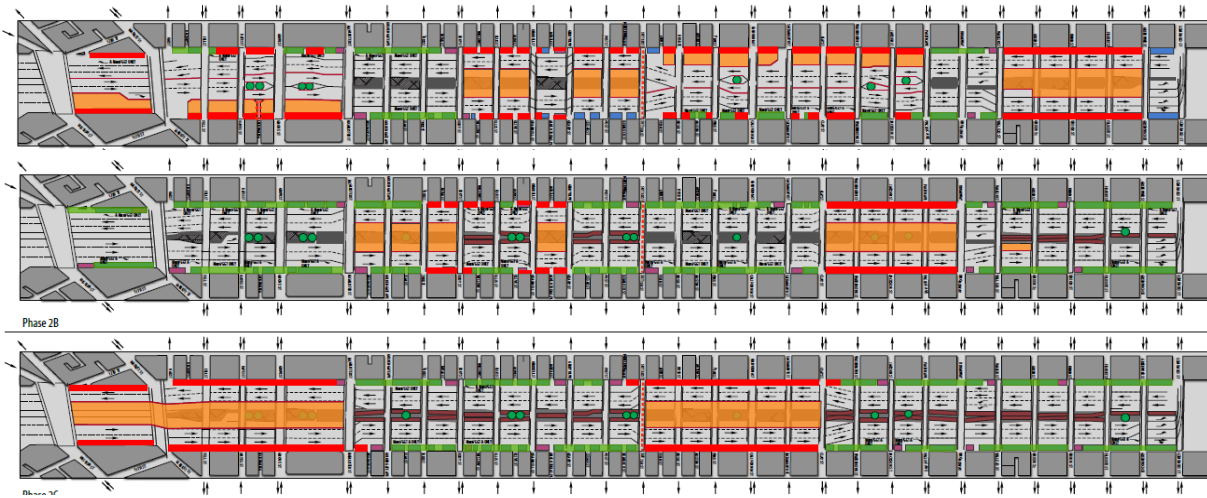

- Phase 3 in progress.



	Start	Finish
1A	Fall 2016	Winter 2022*
1B	Summer 2018	Spring 2021*
1C	Summer 2019	Winter 2022*
1D	Fall 2019	Fall 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Summer 2021 to Fall 2021*

*Estimated

Staff Updates

	Utilities%	Roadway %	Sidewalk %
1A*	100%	100%	95%
1B*	100%	86%	66%
1C*	100%	90%	86%
1D*	100%	77%	70%

- Construction is approximately at 78.02% completion based on expenditures

Staff Updates

Construction update

- BRT buildout

- Construction of red transit lanes, median islands, bus shelters, bulb-outs, overhead lines, trees

- Tentative weekend closure of Mission St. and Market St. intersections in August

Staff Updates

Contract Modification #13

Pays for design revisions

- Modifications to traffic signal layouts
- Additional red-light cameras
- Modifications to the foundations of public artwork at two boarding islands
- Electrical cover plates on boarding islands

Total is \$1.24M, to be funded through existing project budget. This does not extend the length of the project.

Staff Updates

Outreach Updates

- Recent outreach activities
 - Quarterly spring newsletter was sent by mail
- Upcoming outreach activities
 - Quarterly summer newsletter to be sent by email
 - Planning underway for public celebrations at the end of the project
 - Intersection shut down outreach

Staff Updates

Geary Rapid Project

As part of the [Geary Rapid Project](#), work involves replacing aging water infrastructure in continued coordination with San Francisco Public Utilities Commission. Surface transportation improvements are also underway and being managed by San Francisco Public Works, including traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improving median refuges and restriping the newly paved roadway.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Neighboring Project Updates

Caltrans Lombard Street Daytime Lane Closures

Following the [Lombard Vision Zero Project](#), Caltrans recently completed roadway improvements on the US 101/Richardson-Lombard corridor between Francisco Street and Van Ness Avenue. This included repaving the roadway, restriping the lanes and crosswalk and upgrading curb ramps. The SFMTA Board of Directors recently approved High Occupancy Vehicle (HOV) lanes to be added on the corridor. MTA is working with Caltrans to obtain a permit to implement the HOV lanes.

For real-time information, please visit Caltrans QuickMap: quickmap.dot.ca.gov

Member Comment

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

Next Meeting



August 26, 6:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess

