

Vision Zero Quick-Build Project Updates

May 2024

Under Construction



17th Street Quick-Build Project

The 17th Street Quick-Build Project was approved by the San Work continues on the 17th Street Quick-Build Project. During May, SFMTA paint shop crew members began striping the new design onto the roadway. Work includes new striping for floating parking, green bike lane paint, and the addition of vertical deflection in the form of flex posts and rubber curbs. The crew is moving block-by-block with temporary signs posted alerting neighbors of temporary parking restrictions as the work progresses. Substantial work has been installed on 17th street from Mississippi Street to Carolina Street this month.

For more details on the project, please visit: [SFMTA.com/17thStreetQB](https://www.sfmta.com/17thStreetQB)

Recent Outreach


Oak Street Quick-Build Project

The Oak Street Quick-Build project team spent the afternoon on Bike to Wherever Day, talking to people in the Panhandle about the proposed changes for this vital connection in San Francisco's active transportation network. The project proposes a protected eastbound bikeway connecting to the existing bike lane east of Baker Street on Oak Street and complements the existing westbound facilities on Fell Street. The popular Panhandle shared-use path can be crowded at peak times. An alternative eastbound bikeway will create space for people walking and families riding together by offering a parallel facility for faster users and commuters. The project will also improve the safety of walking across the busy Oak Street and better connect Golden Gate Park, the Panhandle, and surrounding neighborhoods.

For more details on the project, please visit: [SFMTA.com/OakQB](https://www.sfmta.com/OakQB)



Recently Approved

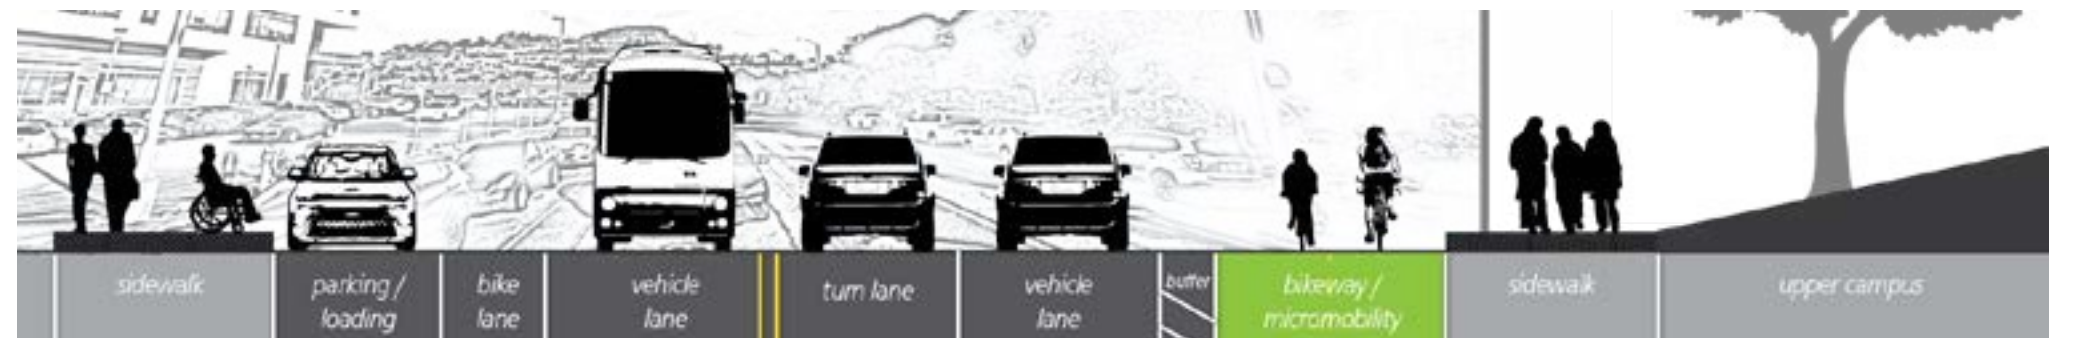

Frida Kahlo Way Quick Build Project

The Frida Kahlo Way Quick-Build Project was unanimously approved by the SFMTA Board of Directors on May 7, 2024. The SFMTA Board requested that project staff return in one year of implementation to provide an update, including evaluation metrics for the project and an update about transit passes for City College of San Francisco students. Construction has begun and will be substantially completed during the summer recess of City College and Riordan High School. Temporary parking restrictions and bus stop relocations will be in effect during the project's construction phase. Approved changes include adding a two-way protected bikeway, building bus boarding islands, transit stop changes, and parking and loading changes.

For more details on the project, please visit: [SFMTA.com/FridaQB](https://www.sfmta.com/FridaQB)

Quick-Build Project Summary Table



Corridor	Scope	Planning/Design Phase	Estimated Construction Phase
Under Construction			
17th Street (Potrero to Pennsylvania)	Protected bikeway, daylighting, painted safety zones, curb management	May 2022 - Fall 2024	Started 4/2024, End Summer 2024
Frida Kahlo Way (Judson to Ocean/Geneva)	Two-way protected bikeway, signal timing changes, transit boarding islands	Jan 2024 - May 2024	Started 5/2024, End Summer 2024
Guerrero Street (Market to 20th)	Pedestrian safety improvements	Jul 2023 - Sep 2023	Start 6/2024, End Summer 2024
Lake Merced Boulevard (Skyline to John Muir)	Protected bikeways, bus boarding islands, bike ramps, lane reduction	Jul 2021 - Jan 2023	Started 9/2023, End 6/2024
Sloat Boulevard (Great Highway to Skyline)	Two-way protected bikeways, painted safety zones, bus boarding islands, parking and loading changes	Sep 2022 - Jul 2023	Start Summer 2024, End Fall 2024
Design in Process			
Alemaný Boulevard (Congdon to Ellsworth)	Two-way protected bikeway, transit boarding island	Jan 2024 - Summer 2024	Mid 2024
Beach Street (Embarcadero to Polk)	Two-way protected bikeways, pedestrian safety improvements, placemaking, signal timing changes	Oct 2023 - Summer 2024	Mid 2024
Cesar Chavez Street (Kansas to Pennsylvania)	Two-way protected bikeways	Jan 2024 - Fall 2024	Late 2024
Clarendon Avenue (Laguna Honda to Johnstone)	Lane reduction, pedestrian safety improvements	Sep 2023 - Spring 2024	Following paving
Larkin Street (Market to Sutter)	Pedestrian safety improvements, lane reduction	May 2024 - Fall 2024	Following paving
Oak Street (Kezar to Baker)	Protected bikeways, signal timing changes, pedestrian safety improvements	Aug 2023 - Fall 2024	Late 2024
Sutter Street (Market to Polk)	Protected bikeways, curb management, lane reduction, pedestrian safety improvements	Aug 2023 - Fall 2024	Late 2024
Completed			
3rd Street (Bay Trail to Townsend Street)	Completed 3/2024	Folsom Street (2nd to 5th)	Completed 5/2021
3rd Street (Berry to Terry Francois)	Completed 7/2020	Franklin Street (Broadway to Lombard)	Completed 12/2022
3rd Street (Mission to Townsend)	Completed 8/2020	Golden Gate Avenue (Market to Polk)	Completed 5/2021
5th Street (Market to Townsend)	Completed 3/2020	Howard Street (Embarcadero to 3rd)	Completed 12/2020
6th Street (Market to Folsom)	Completed 9/2019	Howard Street (3rd to 6th)	Completed 4/2019
7th Street (Folsom to Townsend)	Completed 7/2020	Hyde Street (McAllister to Geary)	Completed 12/2023
7th Street (Townsend to 16th)	Completed 7/2019	Indiana Street (24th to Cesar Chavez)	Completed 11/2019
Alemaný Boulevard (Stoneybrook to Putnam)	Completed 12/2020	Jones Street (O'Farrell to Golden Gate)	Completed 10/2021
Battery Street (Market to Broadway) Sansome Street (Market to Broadway)	Completed 1/2023	Leavenworth Street (McAllister to Post)	Completed 6/2021
Bayshore Boulevard (Oakdale to Industrial)	Completed 9/2023	Lincoln Way (Arguello to Great Highway)	Completed 5/2024
Beale Street (Market to Natoma)	Completed 12/2020	Market Street (Octavia to Steuart)	Completed 1/2020
Brannan Street (Embarcadero to Division)	Completed 11/2019	Mission Street (Trumbull to Geneva) Geneva Avenue (Mission to Prague)	Completed 7/2020
California Street (Arguello to 18th)	Completed 7/2020	South Van Ness Avenue (13th to Cesar Chavez)	Completed 1/2022
The Embarcadero (Bay to North Point, Mission to Harrison)	Completed 12/2020	Taylor Street (Market to Sutter)	Completed 6/2019
The Embarcadero (Mission to Broadway)	Completed 2/2022	Terry Francois Boulevard (Mariposa to Mission Bay)	Completed 8/2019
Evans Avenue/Hunters Point Blvd/Innes Avenue (Jennings to Donahue)	Completed 4/2021	Townsend Street (3rd to 8th)	Completed 9/2020
Evans Avenue (Cesar Chavez to 3rd)	Completed 10/2022	Valencia Street (15th to 23rd)	Completed 8/2023
		Williams Avenue (3rd to Vesta/Phelps)	Completed 10/2021
