

VAN NESS

IMPROVEMENT PROJECT



Van Ness BAC
April 15, 2021



Agenda

1. Call to Order.
2. Public comment: Members of the public may address the Van Ness Business Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.
3. Approval of Minutes – N/A.
4. Presentation, discussion and possible action regarding update from SFMTA staff.
 - Project schedule.
 - Construction update.
 - Business support.
 - Update from Civic Edge on corridor marketing outreach.
 - Update from OEWD on directed business support program.
 - Outreach update.
 - Update on neighboring projects.
5. Adjourn.

BAC administration reminder

- BAC members are asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

Public Comment


- See Public Comment Policy on back of agenda.
- Public comment for matters that are within the Van Ness Business Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes

None.



Staff updates

- Project schedule


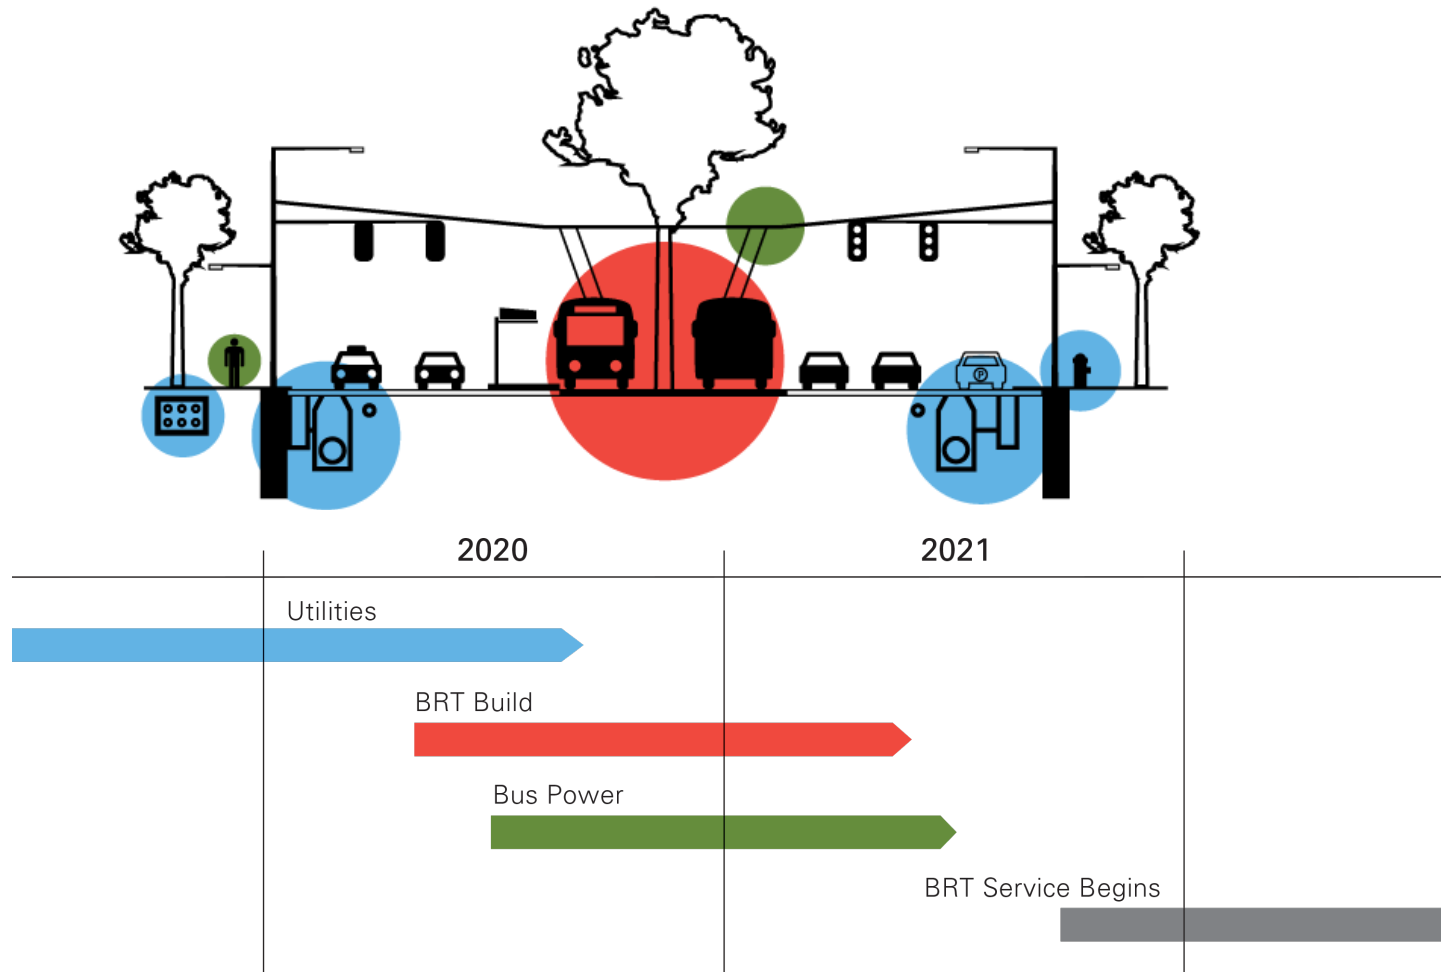


Project Schedule

- Phases 1A and 1B almost complete.



- Phases 1C and 1D almost complete.




	Start	Finish
1A	Fall 2016	Spring 2021*
1B	Summer 2018	Spring 2021*
1C	Summer 2019	Spring 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Winter 2022*


*Estimated

Project Schedule

- Phase 2 in progress.

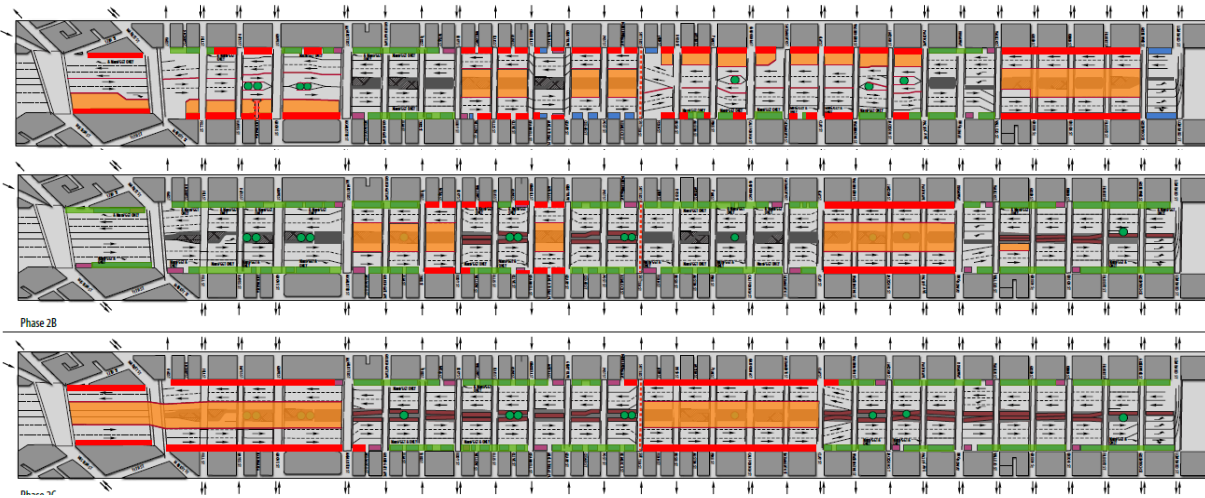

- Phase 3 in progress.

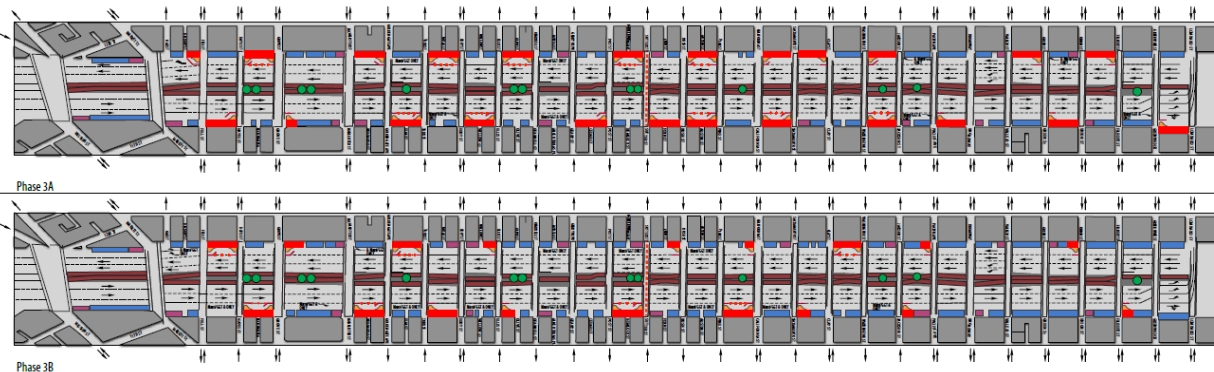

	Start	Finish
1A	Fall 2016	Spring 2021*
1B	Summer 2018	Spring 2021*
1C	Summer 2019	Spring 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Winter 2022*

*Estimated

Staff Updates

Construction update

- BRT Buildout Phase in progress
 - Construction of red transit lanes, median islands, landscaping, bus shelters, bulb-outs, pole setting installations



Staff Updates

- **Business support.**

- New relief for small businesses
 - \$10.9M grants for storefront businesses, amounts range from \$5,000-\$25,000; \$7.3M loan program for businesses, with low to zero-interest loans up to \$100,000. Details on both programs at: sf.gov/sf-relief-grants
 - Have received little to no federal or city funding.
 - Forced to close for 6+ months.
 - Long-established businesses.
 - In high-need neighborhoods.
- Update from Civic Edge on corridor marketing outreach.
- Update from OEWD on directed business support program.

Staff Updates

Outreach Updates

– Recent Activities

- Distribution of Van Ness-branded PPE to corridor businesses

– Upcoming outreach activities

- Quarterly spring newsletter to be sent by mail



Staff Updates

Geary Rapid Project

As part of the [Geary Rapid Project](#), work to replace aging water lines, in coordination with San Francisco Public Utilities Commission, continues. Surface transportation improvements, including upgraded traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improved median refuges and roadway repaving, are also underway and are being managed by San Francisco Public Works.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Neighboring Project Updates

Caltrans Lombard Street Daytime Lane Closures

Follows the Lombard Vision Zero Project and includes repaving the roadway, restriping the lanes and crosswalk and upgrading curb ramps for accessibility. On US-101 (Richardson Avenue at Francisco Street to Lombard at Van Ness Avenue). Construction is through July, Monday through Friday, 7:00 a.m. to 6:00 p.m.

For real-time information, please visit Caltrans QuickMap: quickmap.dot.ca.gov

Next Meeting



August 19, 1:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess

