

VAN NESS

IMPROVEMENT PROJECT



Van Ness BRT CAC

August 22



Agenda

For those calling in, please mute your phones when not speaking by dialing *6. Unmute to speak by dialing *6 again.

1. Call to order. Van Ness BRT Community Advisory Committee members please sit at table.
2. Public comment for matters within Van Ness BRT CAC jurisdiction not on today's calendar.
3. Approval of Minutes – July 25.
4. Better Market Street Presentation by San Francisco Public Works.
5. SFMTA staff updates.
6. Member comment.
7. Adjourn.

CAC administration reminder

- CAC members will be asked to RSVP to confirm quorum
- If no quorum can be reached, meeting to be canceled

Public Comment

- See Public Comment Policy on back of agenda.
- Public comment for matters within the Van Ness BRT Community Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes


- July 25.

Presentation

- Better Market Street presentation by San Francisco Public Works.



Staff updates

- Project update


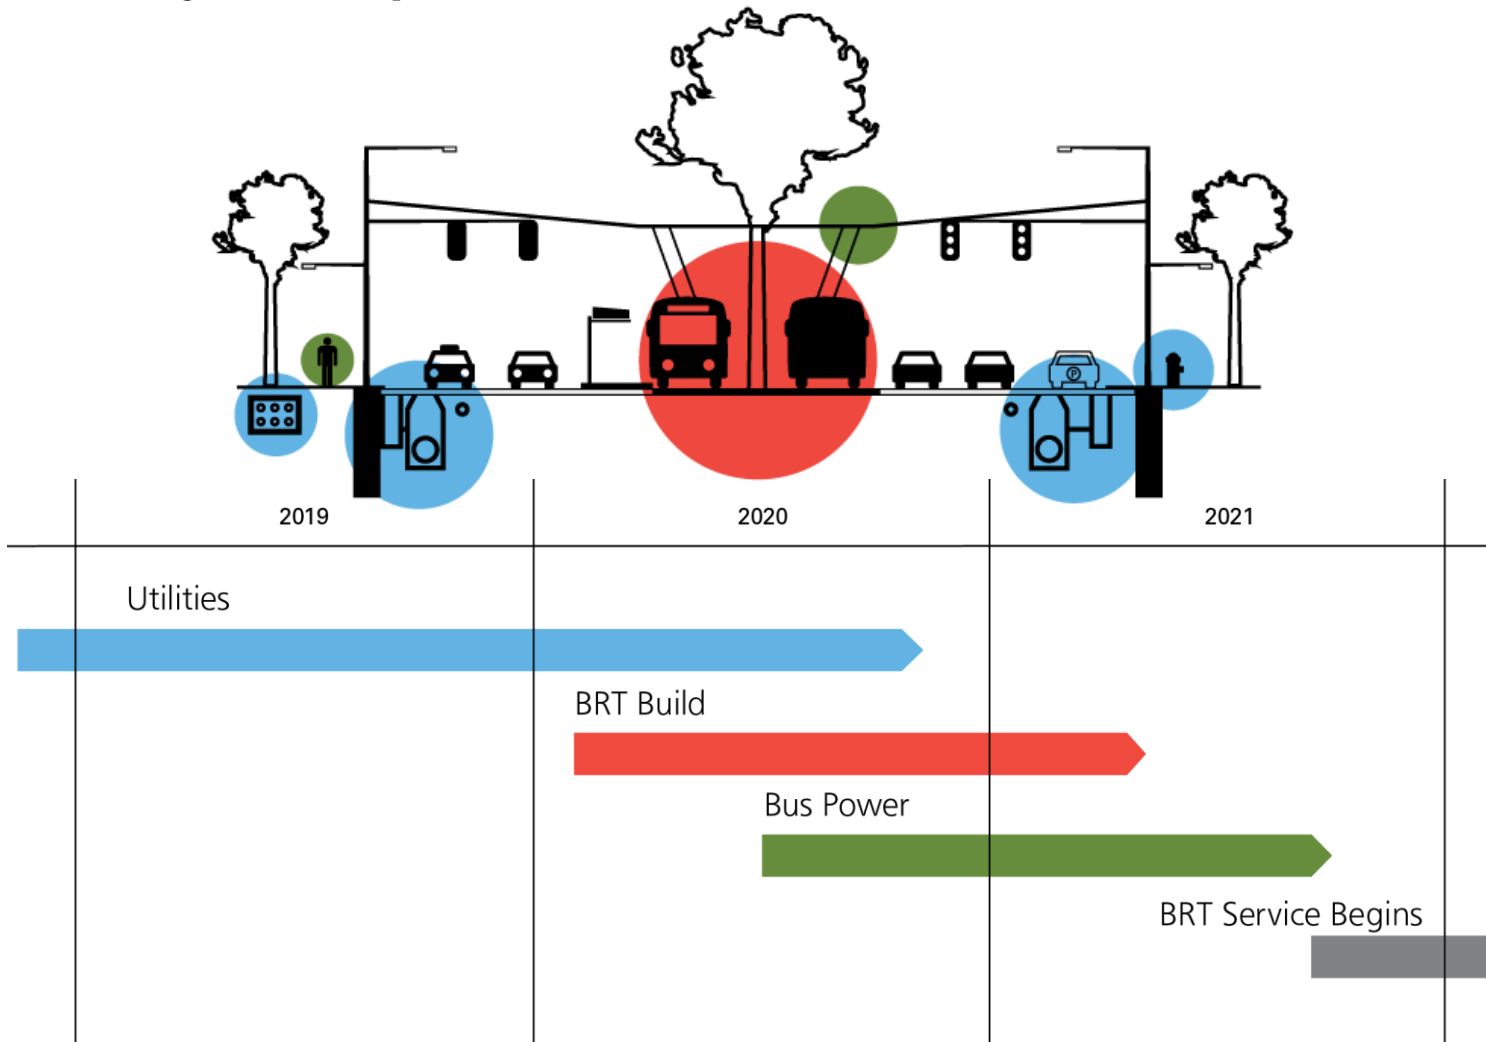


Staff Updates

- Phases 1A and 1B underway. Expected completion winter 2019



- Phases 1C and 1D scheduled summer 2019-summer 2020








	Start	Finish
1A	Fall 2016	Summer 2019*
1B	Summer 2018	Winter 2019*
1C	Summer 2019*	Spring 2020*
1D	Winter 2019*	Summer 2020*
2	Winter 2019*	Spring 2021*
3	Summer 2020*	Summer 2021*

*Estimated

Staff Updates

- Phase 2 scheduled winter 2019-spring 2021



- Phase 3 scheduled summer 2020-summer 2021

	Start	Finish
1A	Fall 2016	Summer 2019*
1B	Summer 2018	Winter 2019*
1C	Summer 2019*	Spring 2020*
1D	Winter 2019*	Summer 2020*
2	Winter 2019*	Spring 2021*
3	Summer 2020*	Summer 2021*

*Estimated

Staff Updates

Construction Updates: Project contract modification approved by MTA Board July 16.

- Resolved two contractor claims for unavoidable delays resulting from water and sewer issues
- Covered by project's allocated allowances, did not increase project budget
 - SFPUC provided analysis and agreed to resolution
 - Increased the contract amount by \$4.8 million
 - Increased contract duration by 279 total calendar days
 - Of claimed 279 days unavoidable delays, 135 days are justifiable due to sewer and water issues
 - Contractor agrees to drop remaining 144 delay days claims and to avoid any litigation cost for both parties

Staff Updates

Construction Updates: Project contract modification approved by MTA Board August 20.

- Resolved claim related to additional potholing for sewer installation necessary to address utility conflicts
- Covered by project's allocated allowances, does not increase project budget
 - SFPUC agrees to resolution
 - Increases the contract amount by \$1.7 million
 - No increase to contract duration

Staff Updates

Construction update

- Joint trenching ongoing
- Addressing utility conflicts
- Sidewalk replacement, street base repair and paving work – outreach to affected blocks ongoing
- SFPD additional nighttime patrols and increased enforcement of construction zones
- Housekeeping team patrolling corridor



Staff Updates

Neighboring projects

- New 79X Chase Center shuttle
 - Begins service September 6



Staff Updates

Geary Rapid Project

The first phase of construction as part of the [Geary Rapid Project](#) continues. Work to replace aging water and sewer lines between Masonic Street and Van Ness Avenue is scheduled to be done in coordination with the San Francisco Public Utilities Commission (SFPUC).

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Staff Updates

Lombard Street Vision Zero Project

The Lombard Street Vision Zero Project includes constructing pedestrian safety and transit performance enhancements as well as utility improvements on US 101 (Lombard Street at Richardson Avenue) between Francisco Street and Van Ness Avenue.

General working hours Monday through Friday 7:00 a.m. to 3:00 p.m.

Project Completion scheduled for: June 2020

For more information visit SFPublicWorks.org/Lombard or call 415-558-5282

Business Support

- Fall Car Card Campaign
- Ideas welcome



VAN NESS IMPROVEMENT PROJECT Support local businesses during construction

GET INSPIRED
Visit Van Ness

San Francisco Symphony musicians

311 Free language assistance / 免費語言協助 / Ayuda gratis con el idioma / Содействие бесплатное переводчиков / Trợ giúp thông dịch miễn phí / Assistance linguistique gratuite / 免費中文翻譯服務 / 免費中文服務 / خط المساعدة اللغوي من الراج

SFMTA.com/VanNess

Logos for various partner organizations including Muni, TA, and others.



VAN NESS IMPROVEMENT PROJECT Support local businesses during construction

GET INSPIRED
Visit Van Ness

San Francisco Symphony musicians

311 Free language assistance / 免費語言協助 / Ayuda gratis con el idioma / Содействие бесплатное переводчиков / Trợ giúp thông dịch miễn phí / Assistance linguistique gratuite / 免費中文翻譯服務 / 免費中文服務 / خط المساعدة اللغوي من الراج

SFMTA.com/VanNess

Logos for various partner organizations including Muni, TA, and others.

Staff Updates

- **Outreach Updates**

- **Recent Activities**

- Meet the Expert, CPMC walking tour August 7
 - Van Ness Business Advisory Committee Meeting, August 15

Staff Updates

- Outreach Updates
 - Upcoming outreach activities
 - SFCTA Citizens Advisory Committee
 - September 4, 6:00 p.m.
 - Meet the Expert
 - September 4, 6:00 p.m.
 - Walking tour of Van Ness Improvement Project
 - Van Ness Business Advisory Committee Meeting
 - September 19, 3:00 p.m.
 - 1 South Van Ness, Civic Center Conference Room, 3rd Floor

Member Comment

- Members of the committee may address the Van Ness BRT Community Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.

Next Meeting



October 24, 6:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

[SFMTA.com/VanNess](https://www.sfmta.com/VanNess)

